



Barrier Berm Project – Daily Report

Day 76

Document: 139551-PMD-076-S

Date Prepared: August 16, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



E4 North Berm – August 15, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 15 August

Vessel	Cubic Yards (CY) Handled	Hopper Loads
East		
Cutter Alaska	19,302	
Cutter Texas	60,300	
Subtotal East	79,602	
West		
Cutter California	44,479	13 Scows
Cutter EW Ellefsen	15,583	
Hopper Stuyvesant	16,336	2
Hopper Liberty Island	9,815	2
Hopper Bayport	7,131	2
Hopper Glen Edwards	19,466	2
Subtotal West	112,810	8
Total	192,412	8

Today – 16 August

- Borrow operations at Pass a Loure and West to continue.
- Berm placement operations to continue on E4 North, E4 South and W9.

Tomorrow – 17 August

- Today's operational activities to continue through tomorrow.


Near-Term Milestones

- Completion of W9 berm construction forecast for 30 August.
- Start of W10 berm construction forecast to begin 6 September.

Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.
- Variations from current fleet configuration.

All Dredges Weekly Volume

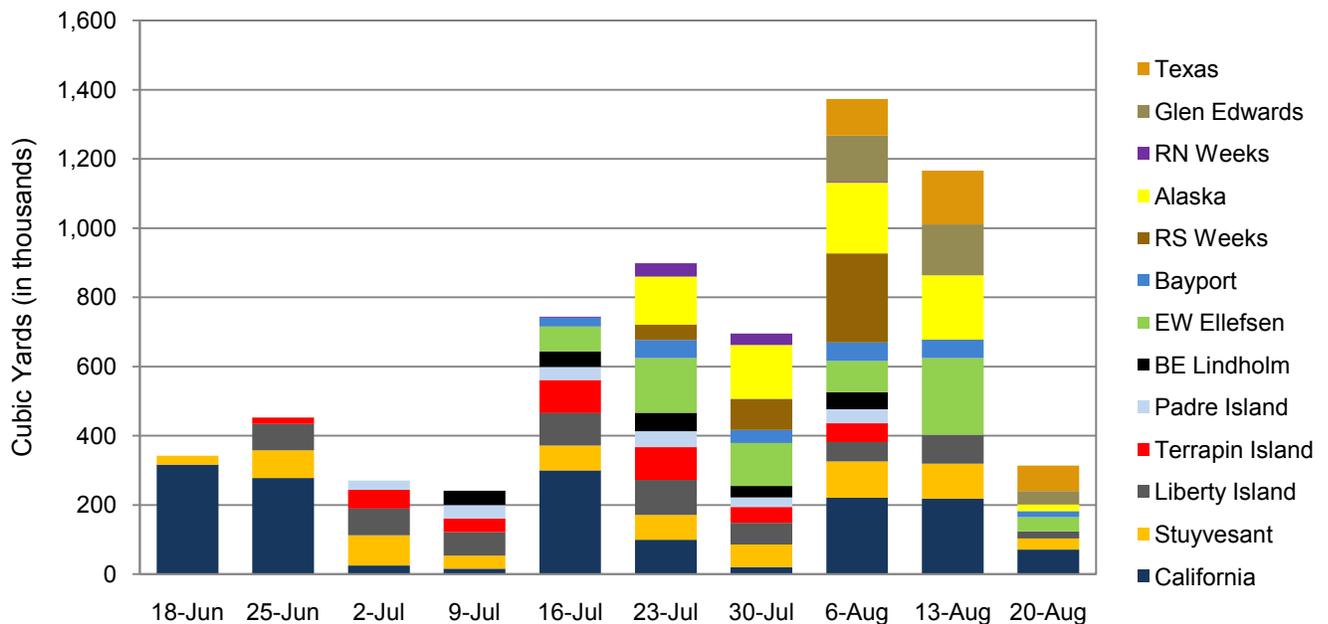

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	1,563,801	
Cutter EW Ellefsen	707,631	
Cutter RS Weeks *	391,350	
Cutter Alaska	703,165	
Cutter Texas	334,065	
Hopper Stuyvesant	677,322	98
Hopper Liberty Island	638,353	141
Hopper Bayport	239,526	62
Hopper Glen Edwards	319,382	31
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	28
Total	6,494,088	639

* Demobilized on or before August 6th.

Progress by Berm and Borrow Operations (cubic yards)

Location	Start	End	Forecast (cy)	Actual (cy)	To Go (cy)	Complete
E3	16-Aug-10	21-Oct-10	3,304,107	0	3,304,107	0.00%
E4	14-Jun-10 A	1-Nov-10	8,345,969	2,071,506	6,274,463	24.82%
W8	6-Sep-10	28-Nov-10	2,802,588	0	2,802,588	0.00%
W9	18-Jul-10 A	27-Aug-10	1,130,870	743,153	387,717	65.72%
W10	24-Aug-10	21-Sep-10	1,327,543	0	1,327,543	0.00%
W11	13-Oct-10	1-Nov-10	1,081,702	0	1,081,702	0.00%
Borrow Operations	16-Jun-10 A	18-Oct-10	13,088,593	3,679,429	9,409,164	28.11%
Totals			31,081,372	6,494,088	24,587,284	20.89%

Note: Percent complete of material handled represents only 1 of 3 elements of percent complete for the overall project.

Progress by Berm (linear feet)

Location	Forecast (LF)	Under Construction (LF)*	To Go (LF)	Complete
E3	35,482	0	35,482	0.00%
E4	80,520	9,330	71,190	11.59%
W8	30,096	0	30,096	0.00%
W9	12,144	3,700	8,444	30.47%
W10	14,256	0	14,256	0.00%
W11	11,616	0	11,616	0.00%
Totals	184,114	13,030	171,084	7.08%

Note: Under normal field conditions, berm is advancing approximately 500 LF per reach per day.

*Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



W9 Berm – August 15, 2010



E4 North Berm – August 15, 2010
