



AMITE RIVER & TRIBUTARIES COMITE RIVER DIVERSION PROJECT

AMITE RIVER BASIN TASK FORCE MEETING

AUGUST 31, 2026



U.S. ARMY



US Army Corps
of Engineers®

Comite River Diversion Canal

Comite River Diversion Overview


(20) USACE contracts

- 20 of 20 contracts awarded
- 15 construction contracts complete
- 5 contracts under construction

(3) LADOTD

- 3 of 3 contracts awarded
- 2 construction contracts complete
- 1 contract under construction

White Bayou Rock Chute

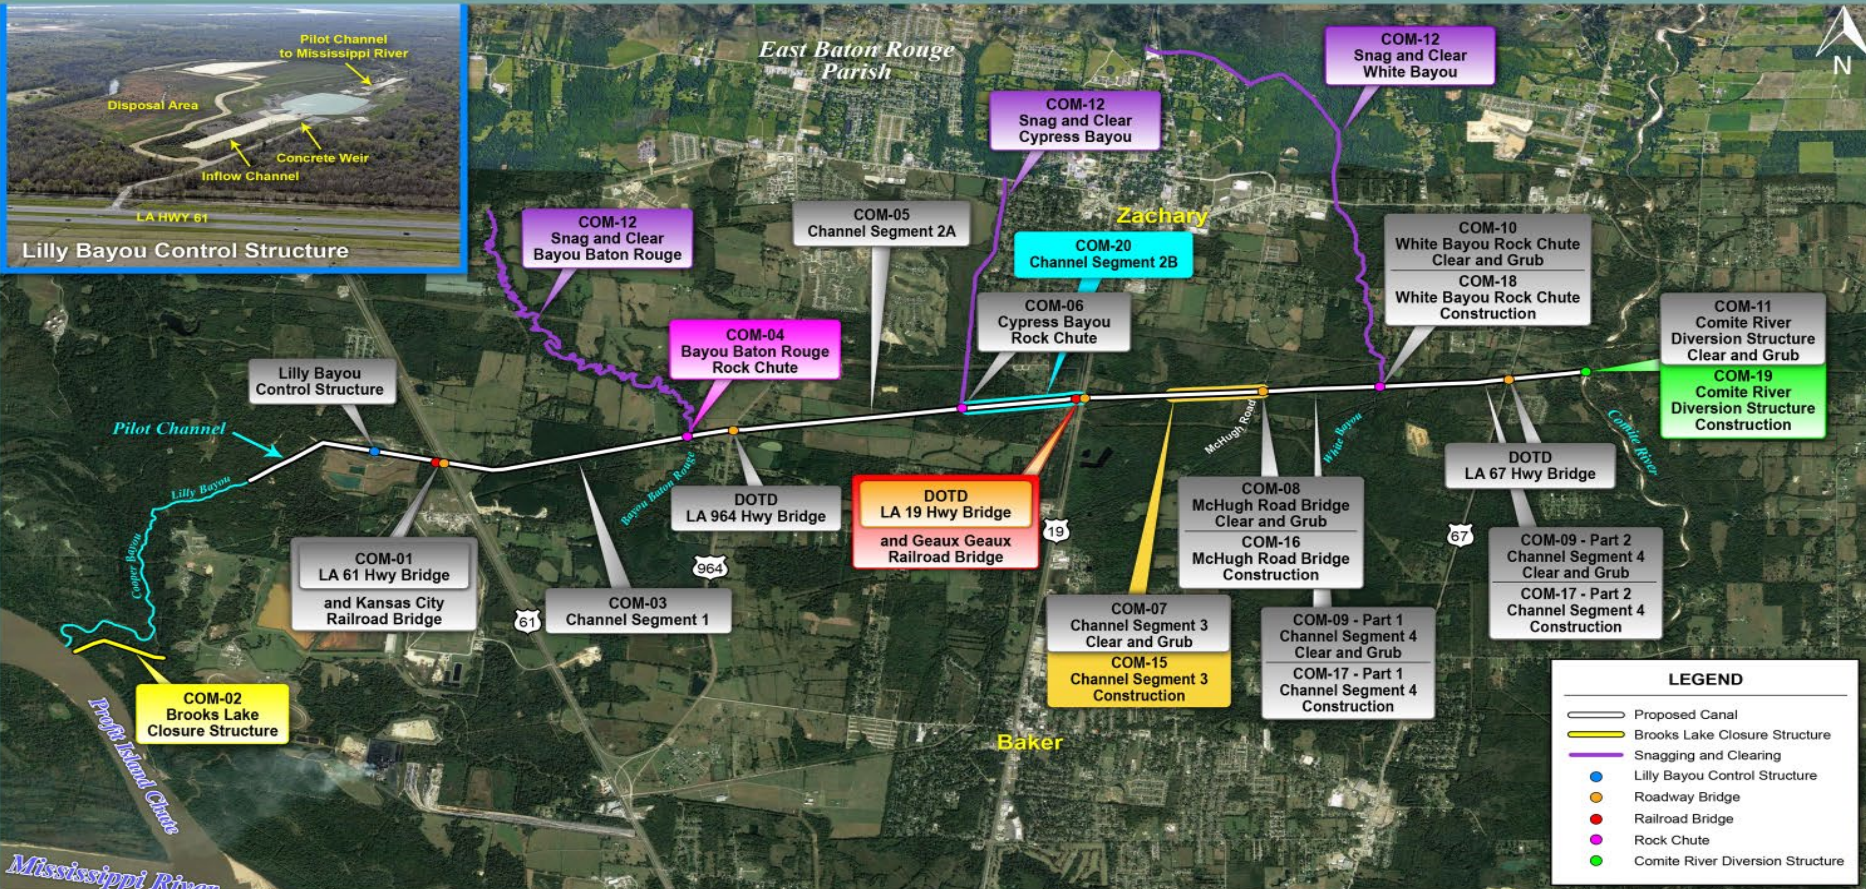

CONSTRUCTION STATUS AND REMAINING CONTRACTS

Brooks Lake



JANUARY 2026 – 3%

Bayou Baton Rouge




JANUARY 2026 – 3%

Channel Segment 2B




JANUARY 2026 – 3%

Channel Segment 3



JANUARY 2026 – 3%

Diversion Structure



JANUARY 2026 – 7%

LADOTD HWY 19



JANUARY 2026 – 17%



COMITE PROGRESS VIDEO



U.S. ARMY



US Army Corps
of Engineers®





FLORIDA GAS RELOCATION AT BROOKS LAKE

- USACE has reviewed and approved the final cost and design from Florida Gas
- The relocation is on schedule to be complete by October 2027



U.S. ARMY



US Army Corps
of Engineers®



PROJECT SCHEDULE

USACE Contract Construction Schedule														
Calendar Year/Quarter														
	2025		2026				2027				2028			
Final Awarded Contracts	3	4	1	2	3	4	1	2	3	4	1	2	3	4
Bayou Baton Rouge	1087 Days Construction (20% Complete)													
Channel Seg #2B	Award					694 Days Construction (22% Complete)								
Channel Segment #3	Award					775 Days Construction (24% Complete)								
Diversion Structure	Award					1006 Days Construction (35% Complete)								
Brooks Lake Closure	Award					455 Days Construction (55% Complete)								
Clearing and Snagging Phase 2	Supplemental EA						Real Estate				Award			
LADOTD - HWY 19	919 days - construction													





QUESTIONS?



U.S. ARMY



US Army Corps
of Engineers®
