
AMITE RIVER AND TRIBUTARIES – COMITE RIVER DIVERSION PROJECT


Briefing to the Amite River Basin Task Force

COL Cullen Jones, P.E. - USACE Christina Brignac, P.E. - LaDOTD

March 21, 2023









Comite River Diversion Project





USACE will deliver 19 construction contracts, to include four main channel segments, two vehicular bridges, one railroad bridge, three rock chutes, diversion structure, and four low flow pumping stations.

LADOTD will deliver 3 construction contracts, to include three vehicular bridges, one railroad bridge, land acquisition, and utility relocations.



COMITE RIVER DIVERSION OVERVIEW



The Project consists of 22 separable contracts:

- 19 USACE Construction Contracts
 - ❖ 13 of 19 contracts awarded
 - **❖** 6 construction contracts are complete
 - ❖ 7 construction contracts are ongoing
 - **❖** 6 remaining contracts
- 3 DOTD Construction Contracts
 - **❖ LA 964**
 - **❖ LA67**
 - **♦ LA19**









COM 01: Hwy 61/ KCS Bridge

(95% Complete)







COM 05: Channel Segment 2A

(75% Complete)

COM 18: White Bayou Rock Chute Phase 2 (70% Complete)









COM 17: Channel Segment 4 Phase 2

(80% Complete)

COM 16: McHugh Road Bridge (90% Complete)









COM 21: Lilly Bayou Phase 2

(95% Complete)





COMITE RIVER DIVERSION PROGRESS



8 of 10 ongoing construction contracts will be complete in CY23

- Channel Excavation: 2 of 4 Segments under construction
 4.3M of 8.4M CY excavated to date
- Vehicular Bridges: 2 of 5 five vehicular bridges are complete.
 Remaining 3 under construction
- Railroad Bridges: 1 of 2 railroad bridges are complete
 Remaining bridge under construction
- * Rock Chutes: 2 of 3 rock chutes under construction



DOTD PROJECT TASKS 2022-2023



Ongoing DOTD tasks

Utility
Relocations:
60+ ongoing
relocations

LA 964
Construction:
diversion road in progress
Award date:
March 24th 2022

Real Estate: 89 Parcels needed 85 Acquired

LA 19 & LA 67-CMAR

Construction LA 67:
diversion road in
progress

LA 67 Awarded date:
March 8th 2022

LA 19 Award date:
December 22, 2022



DOTD CONSTRUCTION CONTRACTS



LA964

(20% Complete)








REAL ESTATE ACQUISITIONS TO DATE-BROOKS LAKE ON-HOLD FOR DESIGN



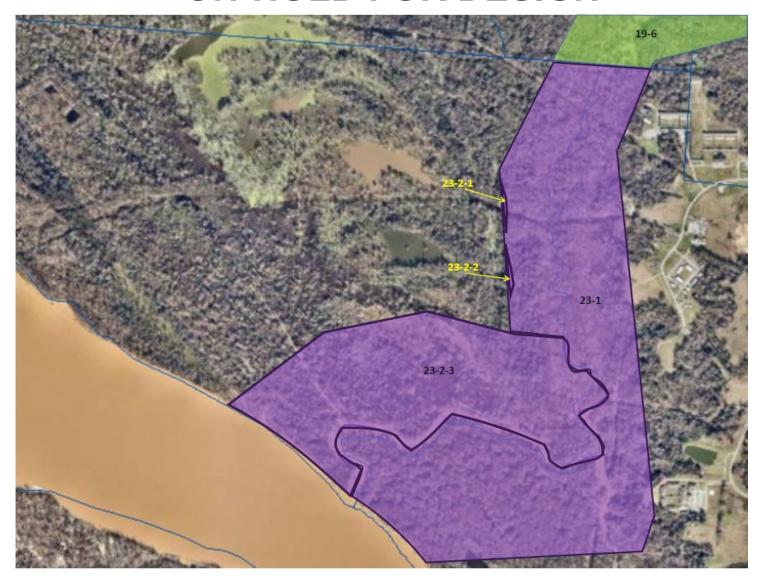



Design change or other delay



REAL ESTATE ACQUISITIONS TO DATE-US 61









REAL ESTATE ACQUISITIONS TO DATE-CHANNEL SEGMENT 1 & BAYOU BATON ROUGE



Status Kev





REAL ESTATE ACQUISITIONS TO DATE- LA 964 & CHANNEL SEGMENT 2






Status Key





REAL ESTATE ACQUISITIONS TO DATE-LA 19 & CHANNEL SEGMENT 3 & MCHUGH RD.



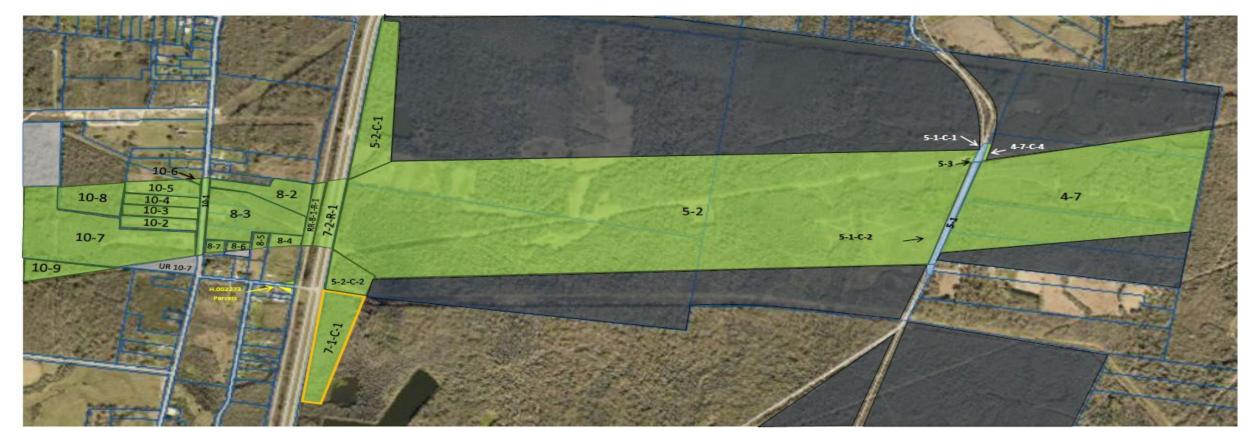







REAL ESTATE ACQUISITIONS TO DATE-CHANNEL SEGMENT 4 & LA 67





Status Key





QUESTIONS



For additional information please contact:



Bobby Duplantier

Bobby Duplantier Qusace army mil



Christina Brignac, F.E.

<u>Christina Brignac Otaleev</u>
