


LOWER ATCHAFALAYA RIVER BAR CHANNEL FY 2016 Maintenance Dredging

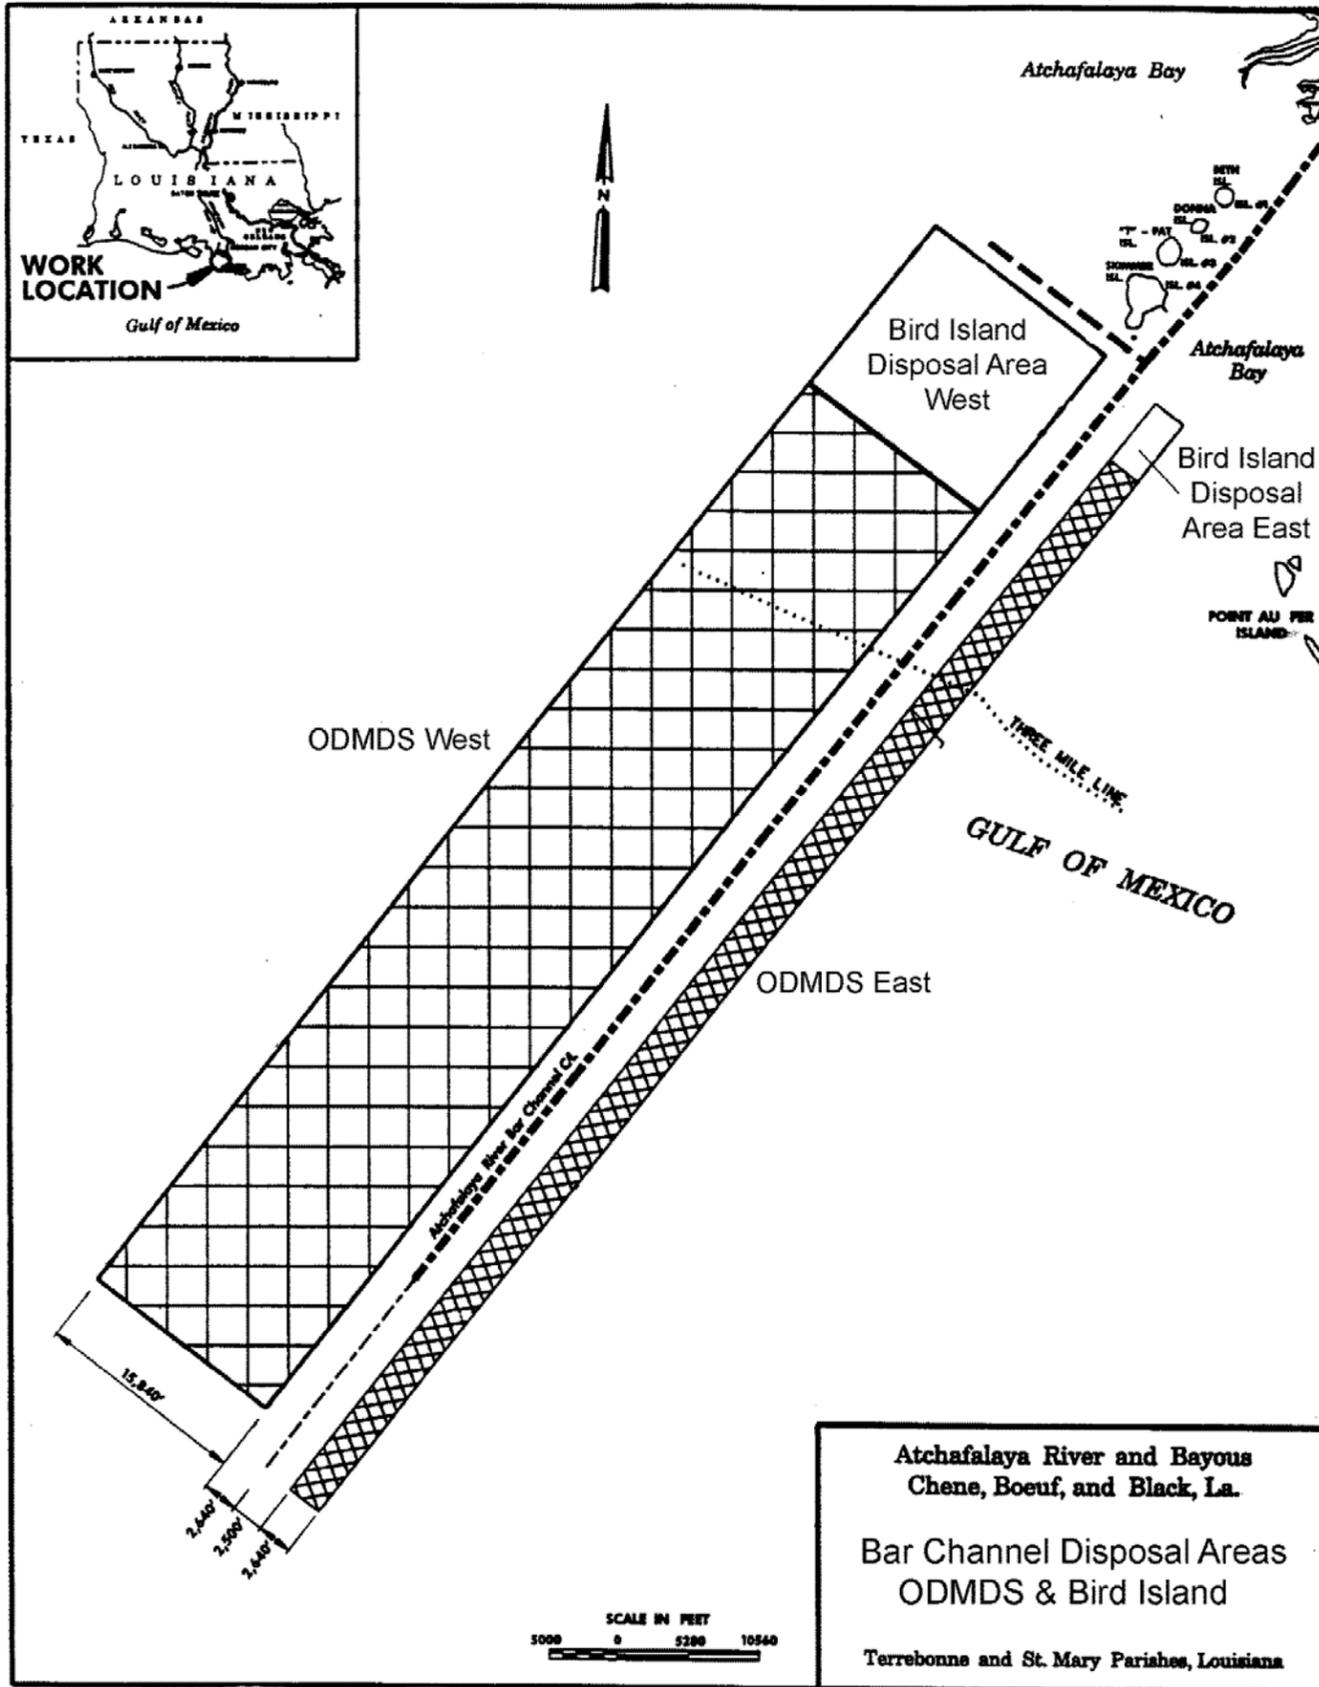

PROJECT	Atchafalaya River and Bayous Chene, Boeuf, and Black, LA
DESCRIPTION OF WORK	Maintain 20' deep x 400' wide channel between Mile 144 to Mile 167 at the 20ft depth contour.
OPERATIONS MANAGER	Mike Lowe: (504) 862-1682
LOCAL SPONSOR	Morgan City Harbor – Terminal District

DREDGING FREQUENCY	Annual
LAST DREDGED	2015
TYPE OF DREDGE USED	Cutterhead

CONTRACT SCHEDULE	Advertise: Jun 2016	Open Bids: TBD	Award: TBD	Start Work: TBD	Duration: 90-210 days
ESTIMATED QUANTITY	9,000,000- 11,000,000 CY				
ESTIMATED COST	\$18,000,000				

DREDGING REACH	Bar Channel Miles 150.6 - 167
DISPOSAL AREAS	Bird Island/ODMDS
DISPOSAL TYPE	Open Water Placement
SEDIMENT CHARACTERISTICS	Sand: 7% Silt: 72% Clay: 21%

REMARKS	Dredged material (sand) placed at Bird Islands. Dredged Material (fluff) discharged in ODMDS about 5000' east or west of the channel.
----------------	--

TYPE of BU PLACEMENT	REASON for NON-BU PLACEMENT
Wetland Creation	Remote Location
<input checked="" type="checkbox"/> Bird Island	<input checked="" type="checkbox"/> Unsuitable Material (Fluff)
Beach Nourishment	Hopper Dredge Required
