

GULF INTRACOASTAL WATERWAY ALGIERS LOCK FOREBAY




FY 2017 MAINTENANCE DREDGING
PROJECT: Gulf Intracoastal Waterway
SUBPROJECT: Algiers Lock Forebay
OPERATIONS MANAGER: Victor Landry
PHONE: (504) 862-2407
LOCAL SPONSOR: U.S. Government has sufficient interest

DESCRIPTION OF WORK:
 Maintain forebay to -12' MLG (with an additional 3' of advance maintenance)

HISTORICAL DREDGING FREQUENCY: Annual
LAST DREDGED: 2014
TYPE OF DREDGE: Cutterhead
ESTIMATED QUANTITY: 40,000 CY
ESTIMATED COST: \$300,000

ADVERTISE: July 2017
OPEN BIDS: TBD
AWARD: TBD
START WORK: TBD
DURATION: 3 days

DREDGING REACH: Lock Forebay
DISPOSAL AREA: Mississippi River
DISPOSAL TYPE: Open Water
REMARKS: Dredged Material Discharged beyond the -55 Depth Contour.
NOTE: This work is done as part of the New Orleans Harbor Contract

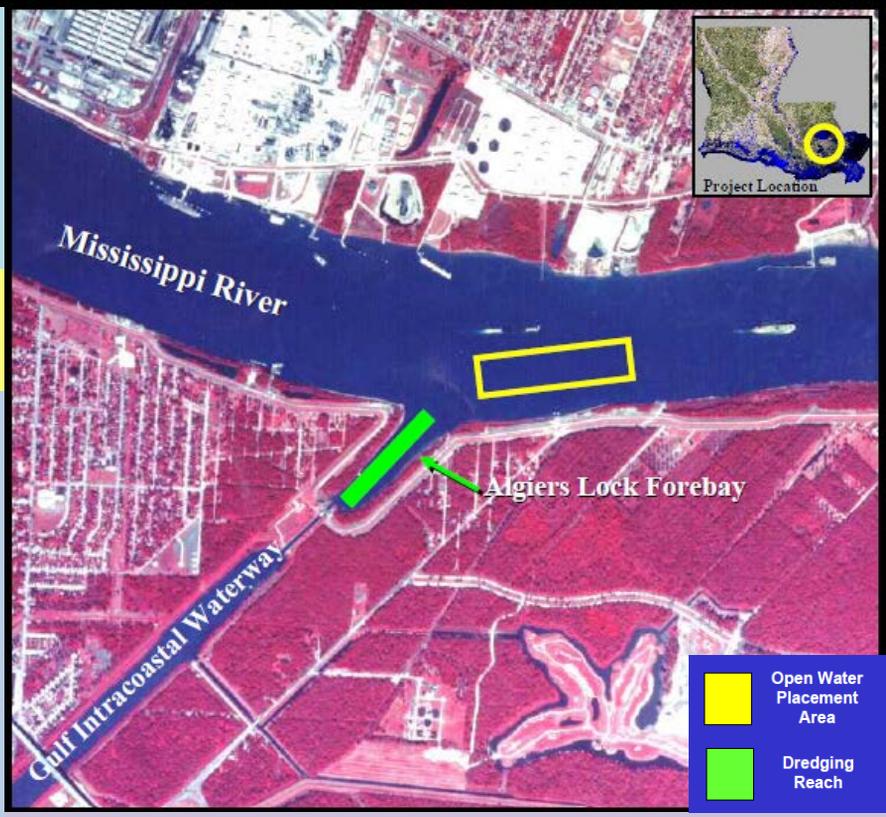

 Open Water Placement Area
 Dredging Reach

GULF INTRACOASTAL WATERWAY ALGIERS LOCK FOREBAY

Fiscal Year	Disposal Area	Dredging Quantity (CY)
2001	Mississippi River Open Water	22,500
2002	Mississippi River Open Water	6,551
		107,008
2003	NO DREDGING	
2004	Mississippi River Open Water	14,807
2005-2007	NO DREDGING	
2008	Mississippi River Open Water	15,415
2009	Mississippi River Open Water	71,886
2010	Mississippi River Open Water	39,706
2011	Mississippi River Open Water	20,138
2012	NO DREDGING	
2013	Mississippi River Open Water	15,408
2014	Mississippi River Open Water	39,719

