

NEW ORLEANS DISTRICT DREDGING SCHEDULE FY 2014



®

US Army Corps of Engineers
BUILDING STRONG®

FY 2014 Scheduled Cutterhead, Dustpan, and Hopper Dredging Work for the New Orleans District




		FY 2014											
Project	Manager	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP
Mississippi River Southwest Pass CDR #1-2014	Kornick												
Calcasieu River Bar Channel #1-2013	Falk												
Mississippi River Southwest Pass #1-2014	Kornick												
Atchafalaya River, Crew Boat Cut Dredging	Lowe												
Mississippi River Southwest Pass #2-2014	Kornick												
Calcasieu River Mi. 5 to 17 and Devil's Elbow	Falk												
Mississippi River New Orleans Harbor, Bayou Lafourche, Houma Navigation Canal, & Baptiste Collette #3-2014	Kornick/Landry/Schneider												
Atchafalaya River Bay, Bar, Crewboat Cut & Miscellaneous Projects	Lowe												
Atchafalaya Basin, GIWW, & Miscellaneous Projects	Lowe/Landry/Beauvais												





MISSISSIPPI RIVER Southwest Pass

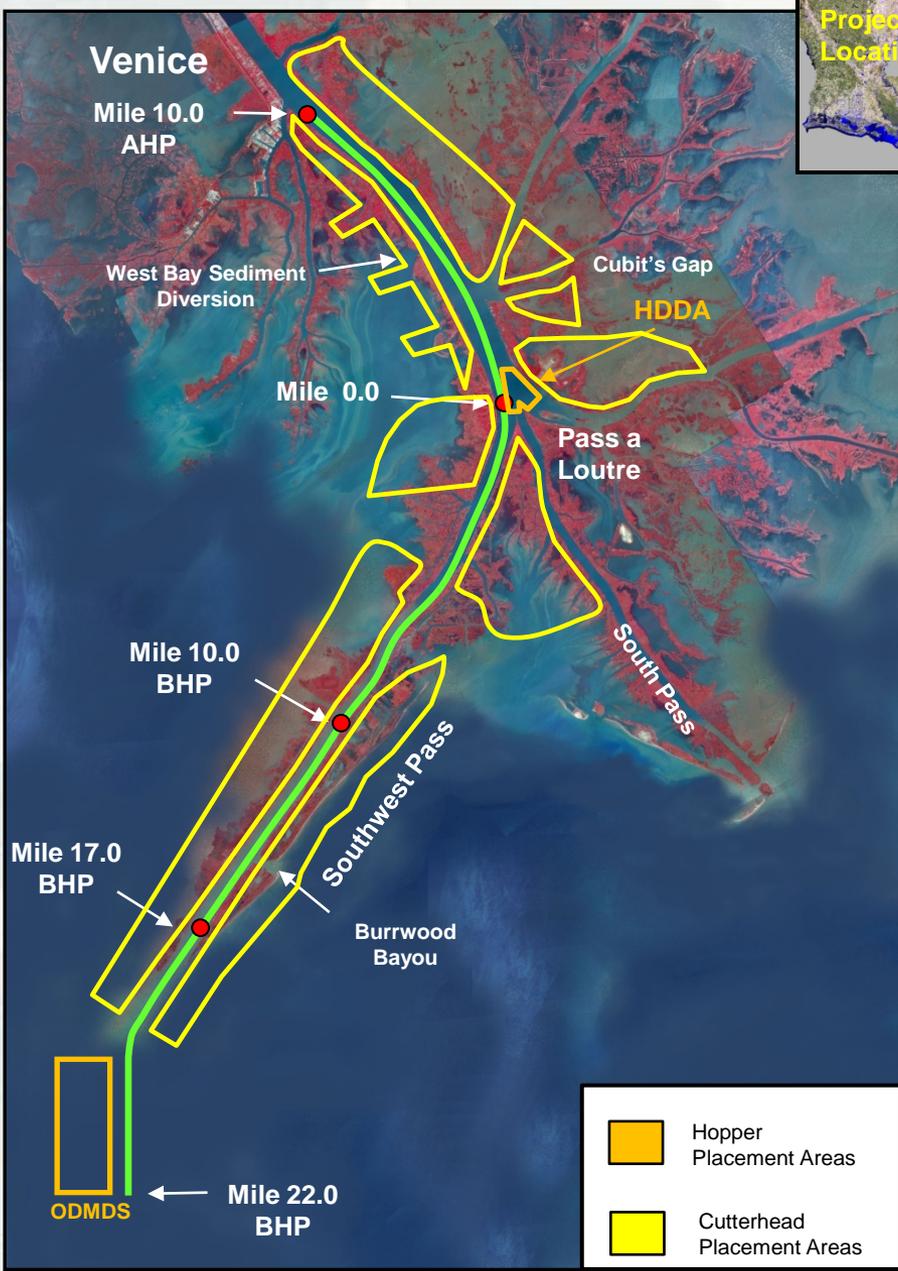

Type of Equipment:

Hopper / Cutterhead

Schedule: Based on River Stage

Depth: 45 ft

Width: 600 ft – 750 ft

Quantity: 17M cy (Annual Avg)

Placement Area:

Open Water/Wetland Development

- HDDA at Head of Passes
- ODMDS
- Shallow open water areas located on either side of the channel


Last Dredged: 2013



MISSISSIPPI RIVER

New Orleans Harbor

Algiers, Harvey & IHNC Lock Forebays

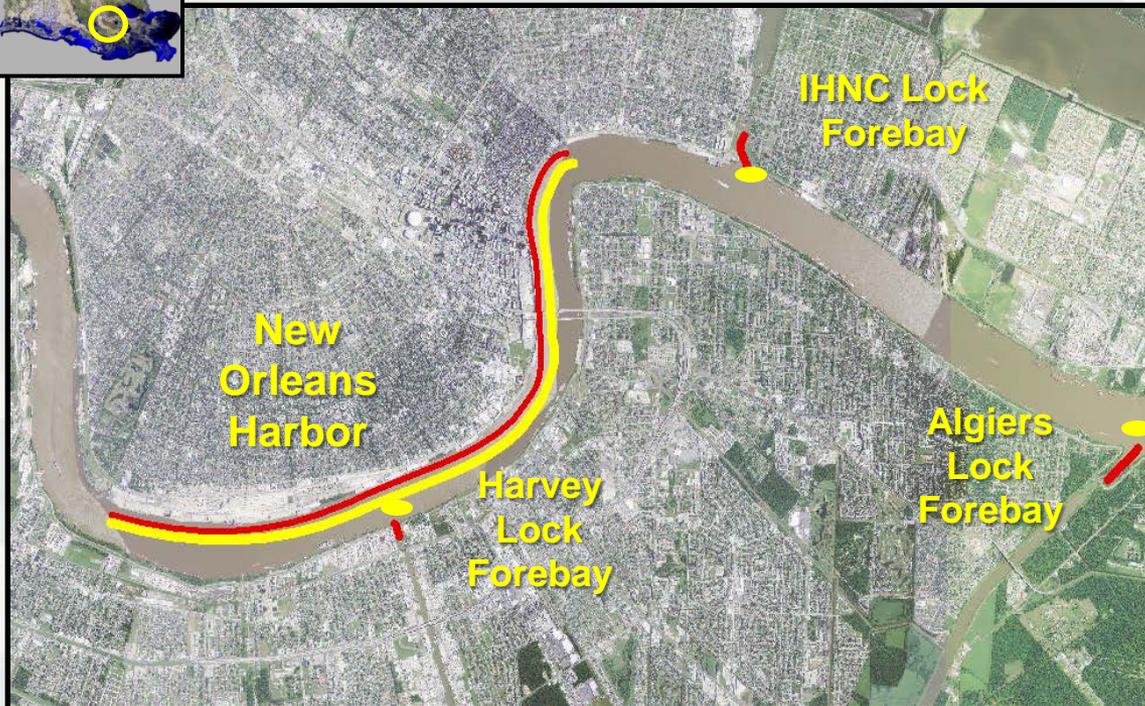

Type of Equipment: Cutterhead

Schedule: Based on River Stage

Depth: Varies by location
15 ft to 35 ft

Quantity: (Annual Avg)
Harbor - 800K cy
Locks - 200K cy

Placement Area: Open Water

Last Dredged: 2013

 Open Water Placement

 Dredging Region




Operations Managers: Mississippi River, Michelle Kornick 504-862-1842
GIWW, Vic Landry 504-862-2407

BUILDING STRONG®



Project Location

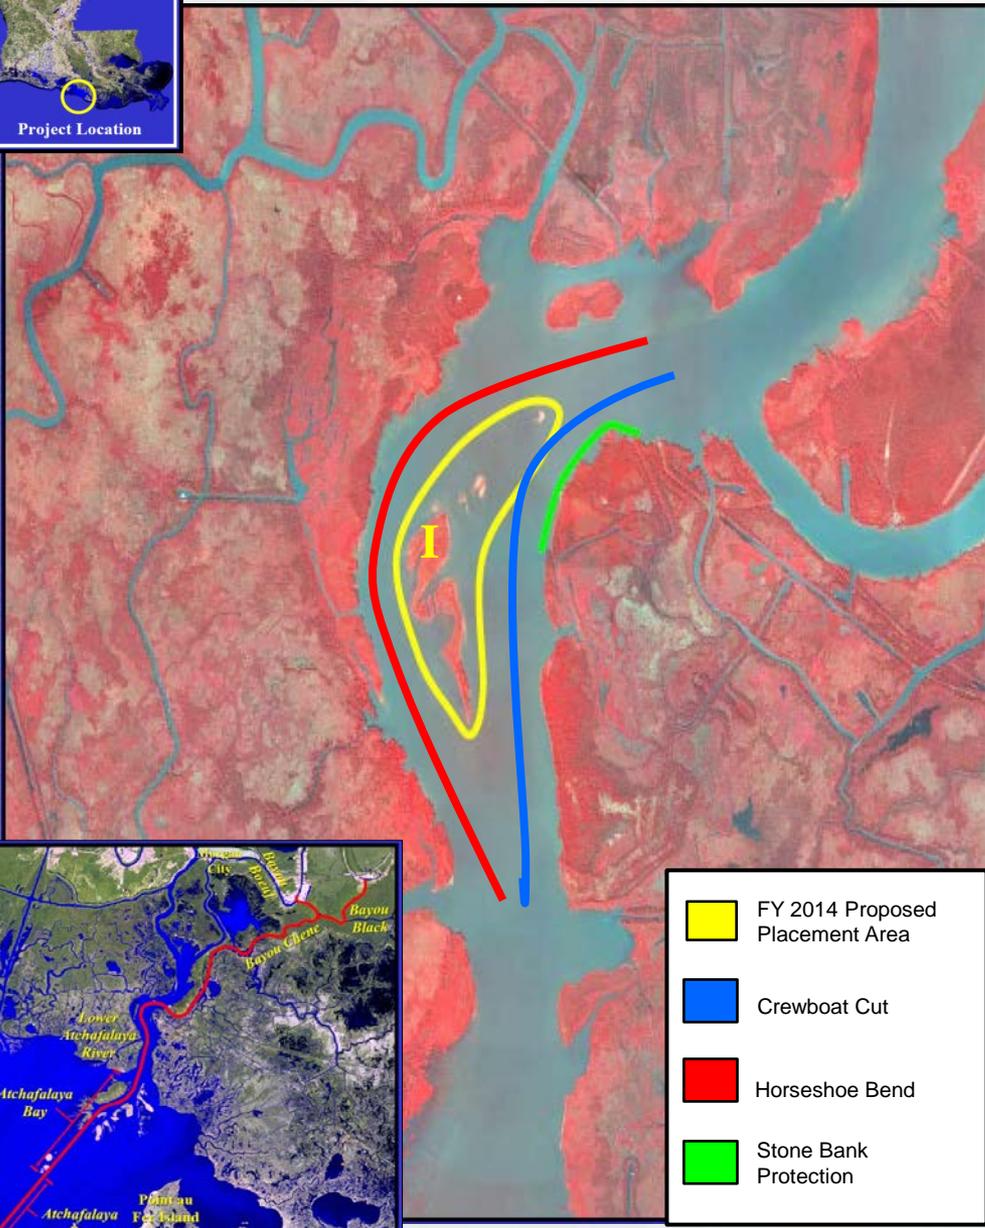

-  FY 2014 Proposed Placement Area
-  Crewboat Cut
-  Horseshoe Bend
-  Stone Bank Protection

ATCHAFALAYA RIVER

Crewboat Cut / Horseshoe

Crewboat Cut: 20 ft x 400 ft x 2700 ft

Type of Equipment: Cutterhead

Scheduled: Mar - Apr 2014


Quantity: 650k cy

Placement Area: Wetland Development


Distance to Placement: 2,000-18,000 ft

Last Dredged: Initial Construction





Bay & Bar Channel

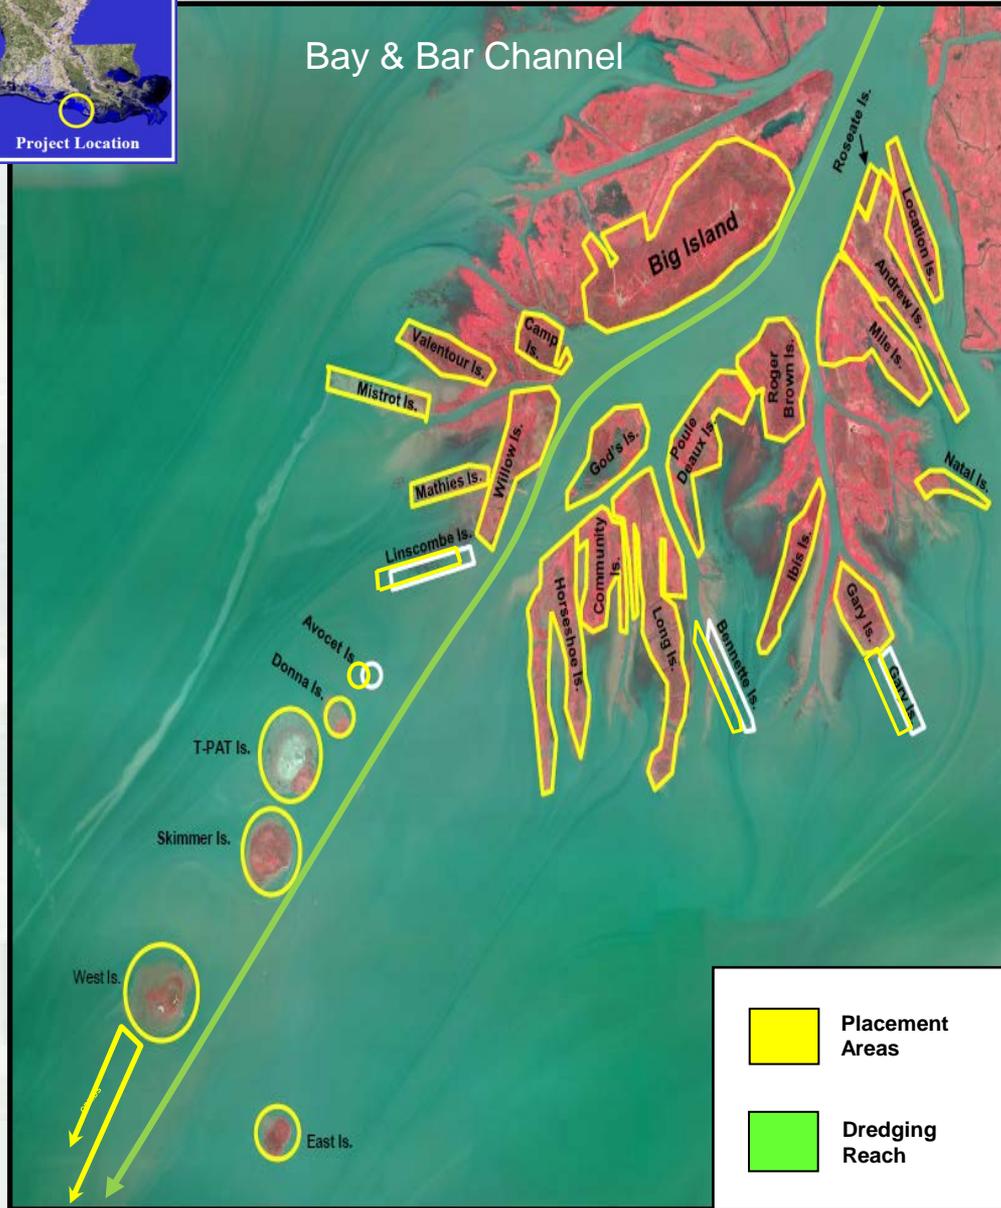

ATCHAFALAYA RIVER

Bay, Bar & Crewboat Cut

Type of Equipment: Cutterhead

Scheduled: Aug - Sep 2014

Quantity: 5M cy

Bay: 20 ft x 400 ft

Placement Area: Open Water Island

Creation

Distance to Placement: 5,000 - 40,000 ft

Bar: 20 ft x 400 ft

Placement Area: Ocean D/A, Bird Island

Distance to Placement: 5,000 ft


Last Dredged: 2012



Operations Manager: Mike Lowe 504-862-1682

BUILDING STRONG®

ATCHAFALAYA BASIN GIWW & MISC PROJECTS

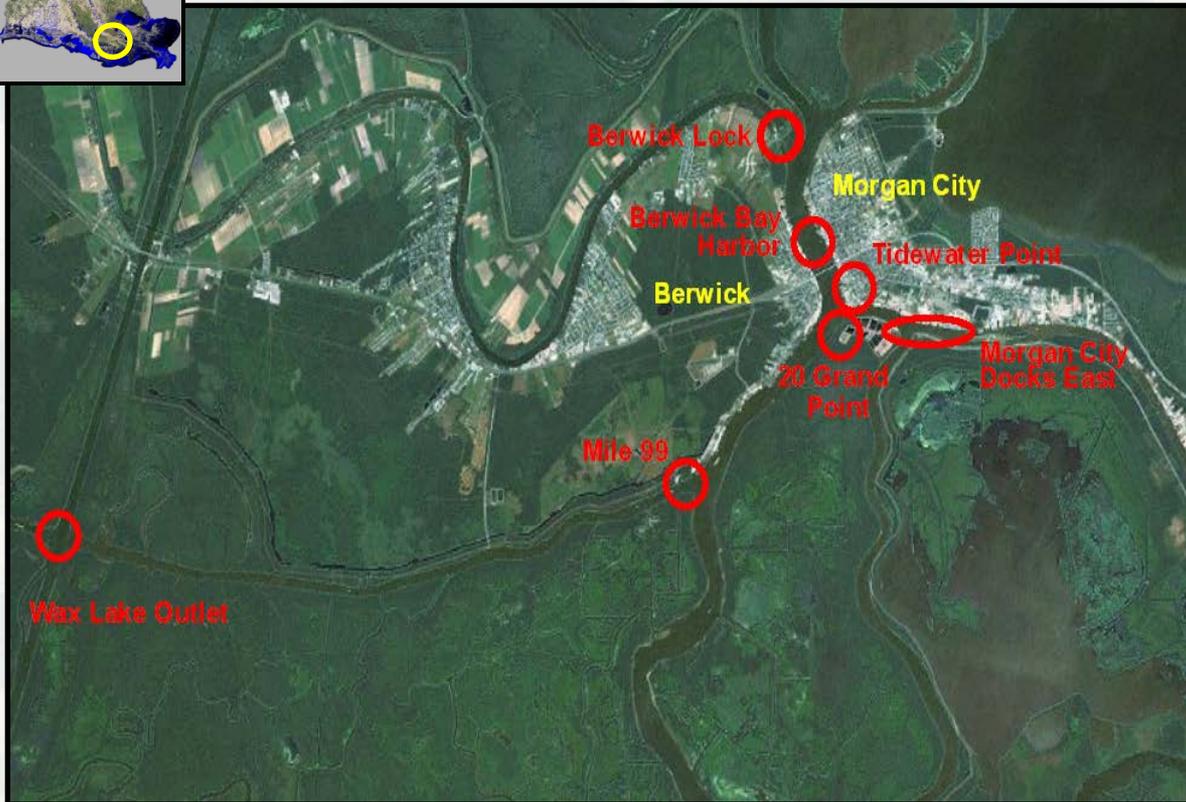

Type of Equipment: Cutterhead

Schedule: Aug - Dec 2014

Depth: 12 ft to 16 ft

Width: Various

Quantity: 1.2M cy

Placement Areas:

Open Water

Sand Pits (Berwick Harbor)

Last Dredged: 2013

Dredging Locations: Berwick Bay Harbor, Berwick Lock, Tidewater Point, 20 Grand Point, Morgan City Docks East, Mile 99, Wax Lake Outlet
(continued on next slide)




Operations Managers: Atchafalaya, Mike Lowe 504-862-1682
GIWW, Vic Landry 504-862-2407
Old River, Russell Beauvais 225-492-2169

BUILDING STRONG®

ATCHAFALAYA BASIN GIWW & MISC PROJECTS (continued)

Dredging Locations: Port Allen Lock Forebay, Baton Rouge Harbor (Devil's Swamp), Old River Lock Forebay & Tailbay and Three Rivers

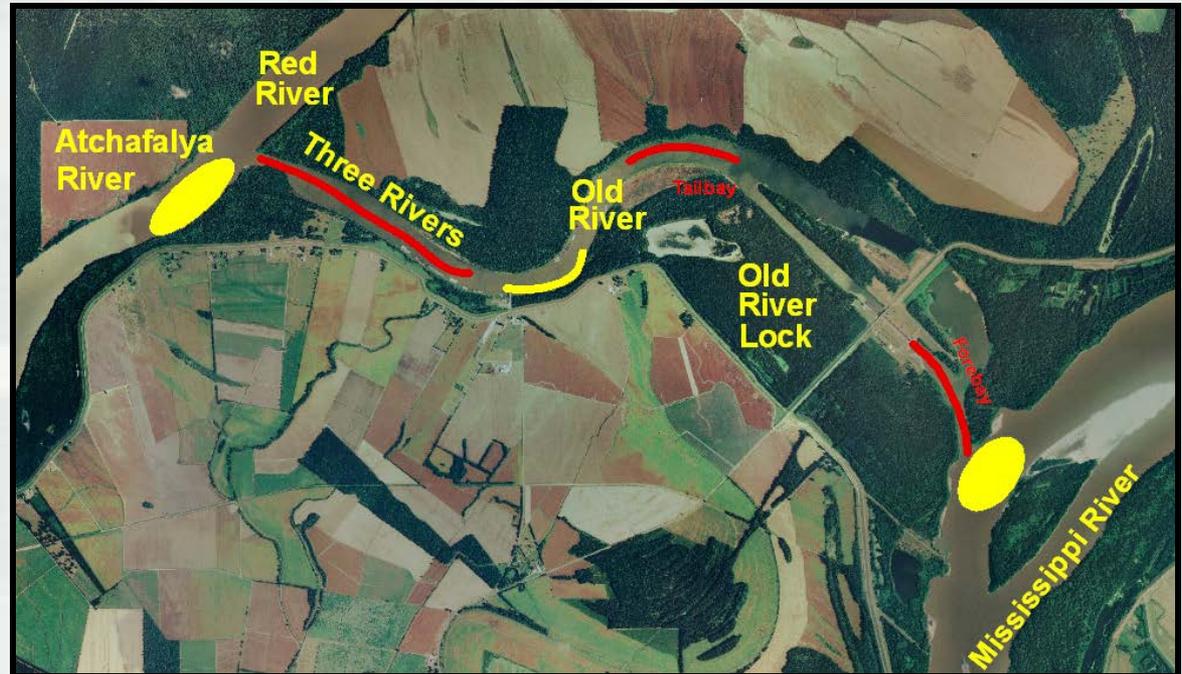


-  Open Water Placement
-  Dredging Region



Operations Managers: Atchafalaya, Mike Lowe 504-862-1682
GIWW, Vic Landry 504-862-2407
Old River, Russell Beauvais 225-492-2169

BUILDING STRONG®

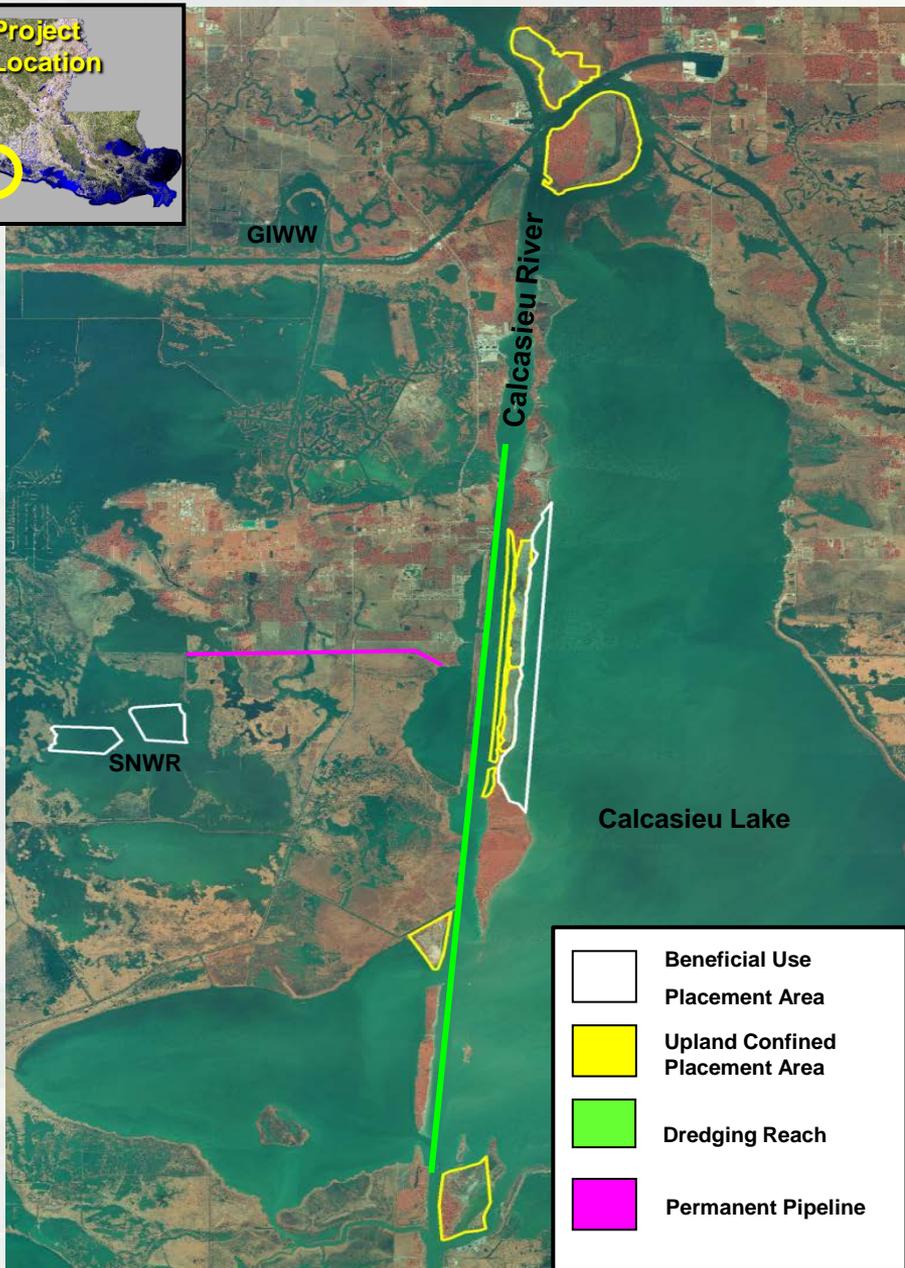

CALCASIEU RIVER

Vicinity Miles 5 – 17
& Devil's Elbow

Type of Equipment: Cutterhead

Schedule: May - Dec 2014

Depth: 40 ft

Width: 400 ft

Quantity: 4M cy


Placement Area: Upland CDF's,
Wetland Restoration (SNWR*)

Last Dredged: 2012

*SNWR = Sabine National Wildlife Refuge



Project
Location

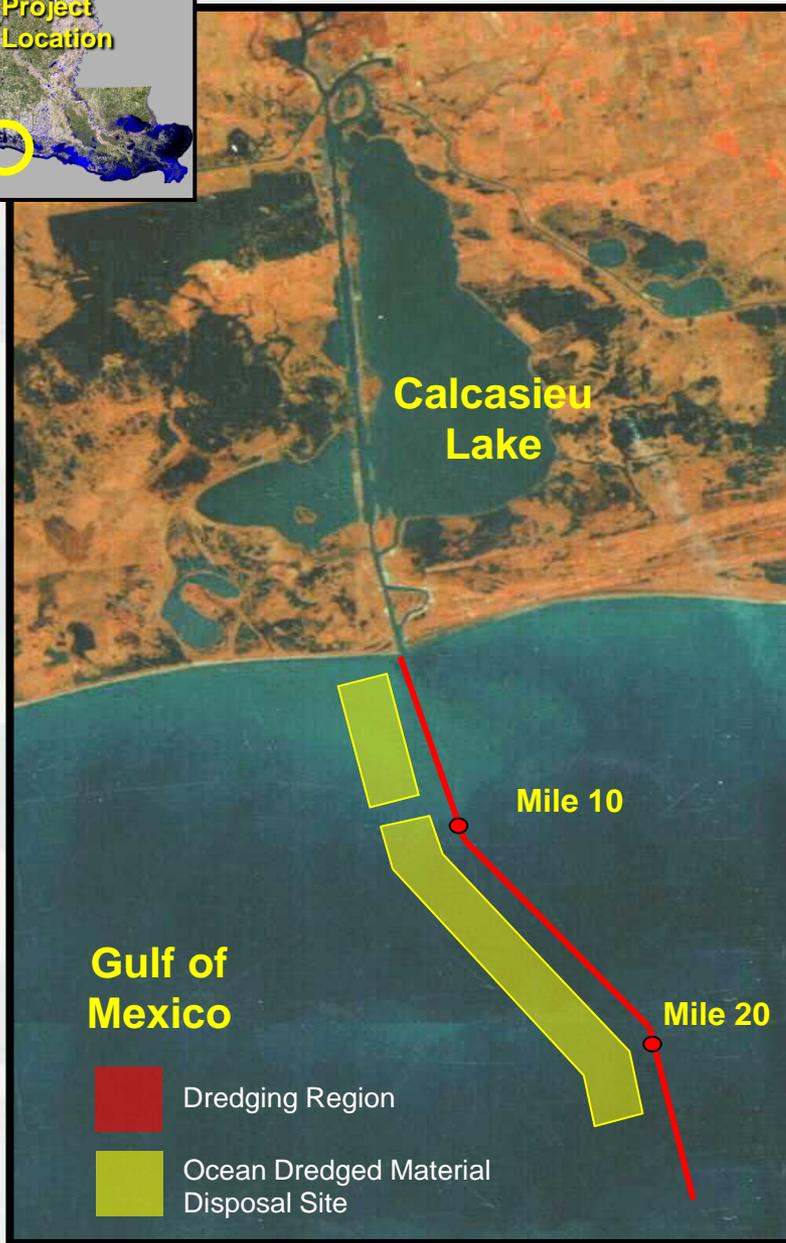

CALCASIEU RIVER

Bar Channel

Type of Equipment: Hopper

Schedule: Feb - May 2014

Depth: 42 ft

Width: 800 ft

Quantity: 7M cy

Placement Area: Agitation & ODMDS

Last Dredged: 2013



Operations Manager: Tracy Falk 504-862-2971


BUILDING STRONG®

HOUMA NAVIGATION CANAL

CANAL

Terrebonne Bay & Cat Island Pass

Mississippi River New Orleans Harbor,
Bayou Lafourche, Houma Navigation Canal,
Baptiste Collette #3-2014

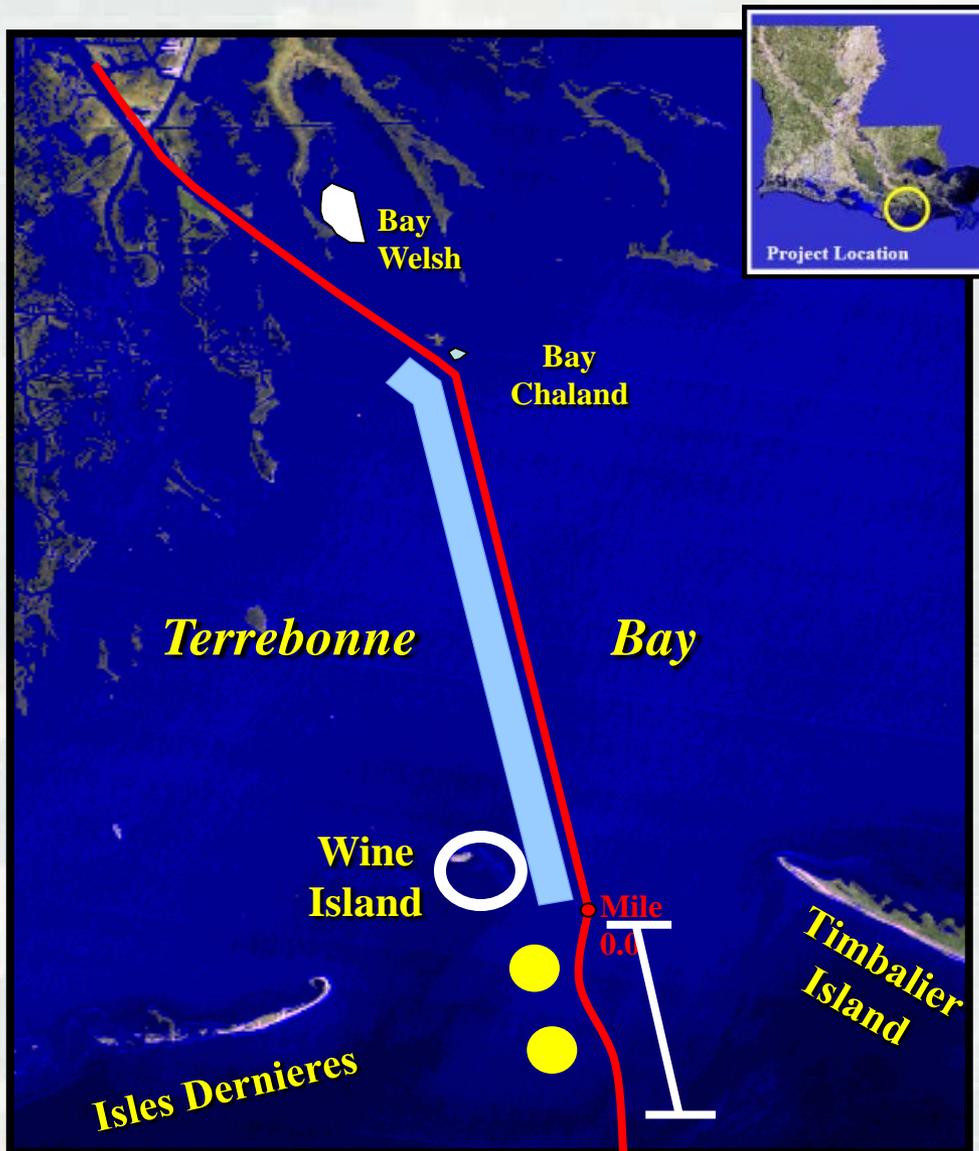

-  Houma Navigation Canal
-  Open Water Disposal Area
-  Single Point Discharge Sites

Type of Equipment: Cutterhead

Schedule: Sept 2014

Depth: 17 ft – 22 ft

Width: 150 ft – 300 ft

Quantity: 300K cy

Placement Area: Open Water

/SPD/Barrier Island Restoration

Distance to Placement Area:

2,000 ft – 5 Mi.

Last Dredged: 2013



Operations Manager: Donald Schneider 504-862-1828

BUILDING STRONG®



Project Location

BAPTISTE COLLETTE

Bar Channel

Mississippi River New Orleans Harbor,
Bayou Lafourche, Houma Navigation Canal,
Baptiste Collette #3-2014

Type of Equipment: Cutterhead

Schedule: Sep 2014

Depth: 16 ft – 18 ft

Width: 150 ft – 250 ft

Quantity: 300K cy

Placement Area:

Wetlands Development/Bird Island

Distance to Placement Area:

2000 ft – 3 Miles

Last Dredged: 2013



Operations Manager: Donald Schneider 504-862-1828

BUILDING STRONG®
