

GULF INTRACOASTAL WATERWAY

WAX LAKE OUTLET



FY 2023 MAINTENANCE DREDGING

PROJECT: Gulf Intracoastal Waterway

SUBPROJECT: Wax Lake Outlet Crossover

OPERATIONS MANAGER: Victor Landry

PHONE: (504) 862-2407

LOCAL SPONSOR: U.S. Government has
sufficient interest

COASTAL ZONE MANAGEMENT: C20220122

DESCRIPTION OF WORK:

Maintain 12' x 125' channel at the
intersection of the GIWW and the Wax
Lake Outlet (with an additional 3' of
advance maintenance)

HISTORICAL DREDGING FREQUENCY: Annually

LAST DREDGED: 2021

TYPE OF DREDGE: Dustpan

ESTIMATED QUANTITY: 220,000 CY

ESTIMATED COST: \$380,000

ADVERTISE: TBD

OPEN BIDS: TBD

AWARD: TBD

START WORK: TBD

DURATION: 7-10 Days

DREDGING REACH: Intersection of GIWW and
Wax Lake Outlet

DISPOSAL AREA: Wax Lake Outlet


DISPOSAL TYPE: Open Water

REMARKS: Dredged Material discharged
beyond the -32' Depth Contour



WAX LAKE OUTLET

Fiscal Year	Disposal Area	Dredging Quantity (CY)
2001	Wax Lake Outlet Open Water	63,319
		86,164
2002	Wax Lake Outlet Open Water	141,562
		122,607
2003	Wax Lake Outlet Open Water	131,604
2004	Wax Lake Outlet Open Water	173,005
2005	Wax Lake Outlet Open Water	88,964
2006	Wax Lake Outlet Open Water	17,393
2007	Wax Lake Outlet Open Water	141,100
2008	Wax Lake Outlet Open Water	119,800
2009	Wax Lake Outlet Open Water	251,479
2010	Wax Lake Outlet Open Water	133,115
2011	Wax Lake Outlet Open Water	95,781
2013	Wax Lake Outlet Open Water	193,741
2015	Wax Lake Outlet Open Water	164,527
2016	Wax Lake Outlet Open Water	100,259
2018	Wax Lake Outlet Open Water	489,633
2020	Wax Lake Outlet Open Water	216,480
2021	Wax Lake Outlet Open Water	85,333

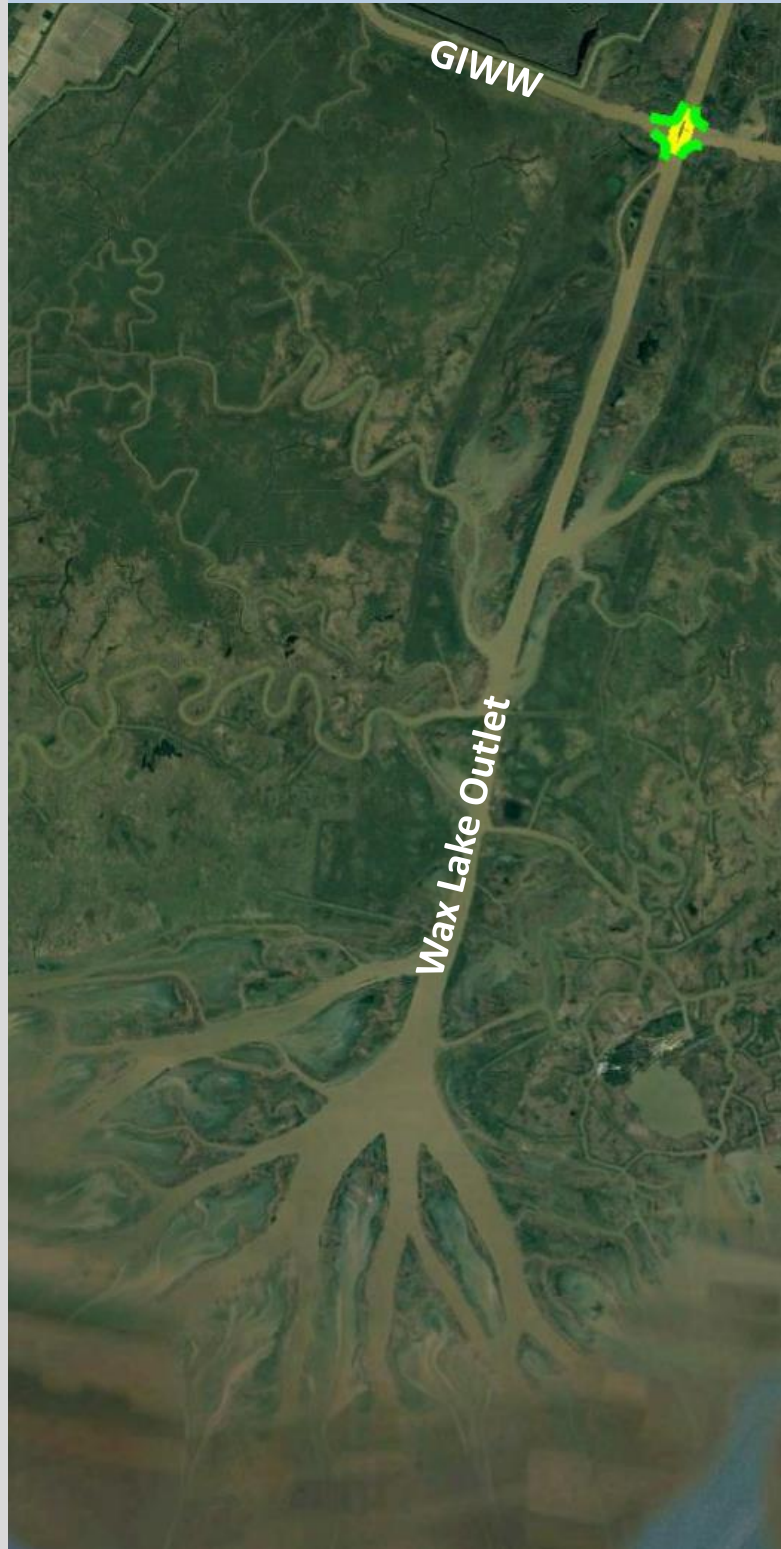

Dredging Reach



Open Water Placement Area
