


**GULF INTRACOASTAL WATERWAY
ALTERNATE ROUTE
BELOW BAYOU SORREL LOCK
FY 2016 Maintenance Dredging**

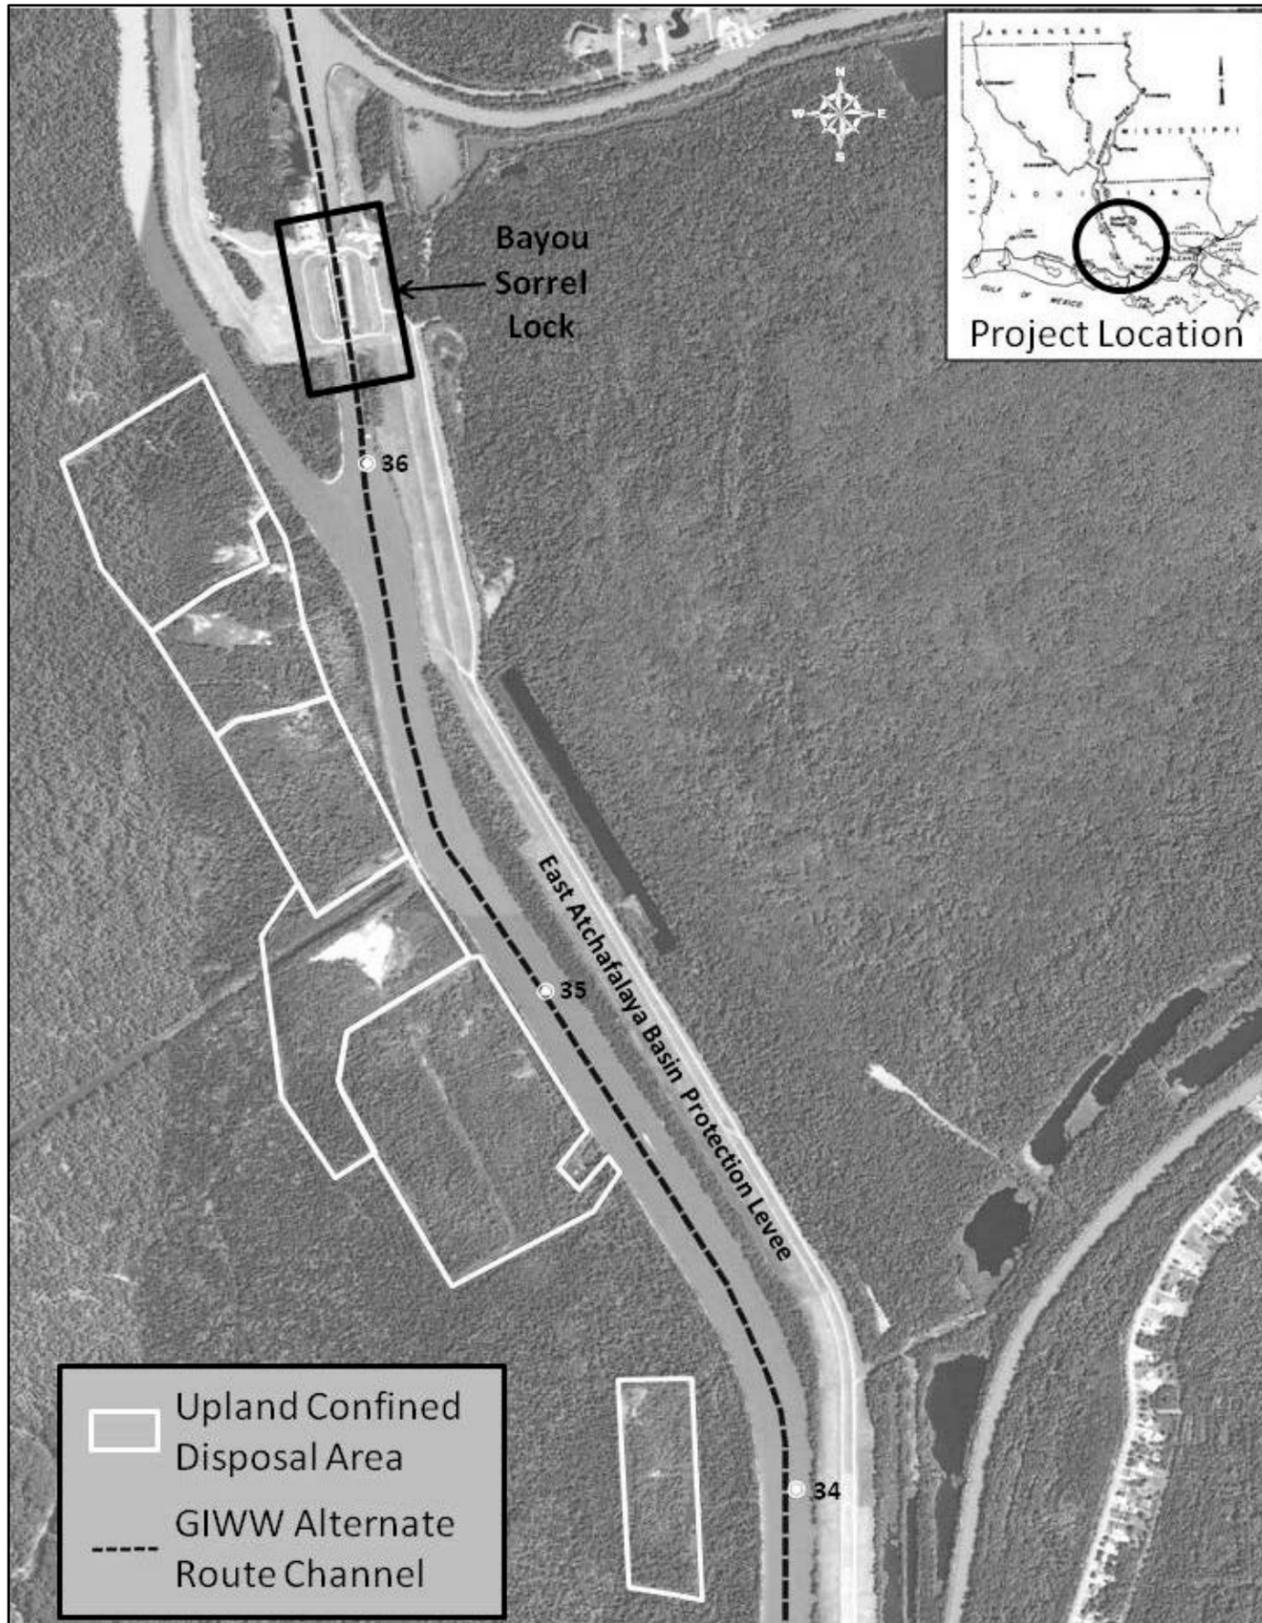

PROJECT	Gulf Intracoastal Waterway, LA - Port Allen to Morgan City Alternate Route		
DESCRIPTION OF WORK	Maintain 12' deep x 125' wide channel from Mile 33 to 37 below Bayou Sorrel Lock (with an additional 3' of advance maintenance)		
OPERATIONS MANAGER	Victor Landry (504-862-2407)		
LOCAL SPONSOR	U.S. Government has sufficient interest		

DREDGING FREQUENCY	As Needed
LAST DREDGED	2011
TYPE OF DREDGE USED	Cutterhead or Bucket Dredge

CONTRACT SCHEDULE	Advertise: May 2016	Open Bids: TBD	Award: TBD	Start Work: TBD	Duration: 21 days
ESTIMATED QUANTITY	300,000 CY				
ESTIMATED COST	\$1,500,000				

DREDGING REACH	GIWW Alternate Route Mile 33-37
DISPOSAL AREAS	Upland Confined Disposal Facilities (located adjacent to the channel)
DISPOSAL TYPE	Upland Confined
SEDIMENT CHARACTERISTICS	Sand: % Silt: % Clay: %

TYPE of BU PLACEMENT	REASON for NON-BU PLACEMENT
Wetland Creation	X Remote Location
Bird Island	Unsuitable Material (Fluff)
Beach Nourishment	Hopper Dredge Required
