

FY 2015 MAINTENANCE DREDGING

PROJECT: Gulf Intracoastal Waterway
SUBPROJECT: Wax Lake Outlet Crossover
OPERATIONS MANAGER: Victor Landry
PHONE: (504) 862-2407
LOCAL SPONSOR: U.S. Government has sufficient interest

DESCRIPTION OF WORK:


Maintain 12' x 125' channel at the intersection of the GIWW and the Wax Lake Outlet (with an additional 3' of advance maintenance)

HISTORICAL DREDGING FREQUENCY: Annually
LAST DREDGED: 2013
TYPE OF DREDGE: Cutterhead/ Bucket
ESTIMATED QUANTITY: 200,000 CY
ESTIMATED COST: \$700,000

ADVERTISE: Jan 2015
OPEN BIDS: Depends on River Conditions
AWARD: TBD
START WORK: TBD
DURATION: 7-10 days

DREDGING REACH: Intersection of GIWW and Wax Lake Outlet
DISPOSAL AREA: Wax Lake Outlet
DISPOSAL TYPE: Open Water
REMARKS: Dredged Material discharged beyond the -32' Depth Contour

GULF INTRACOASTAL WATERWAY WAX LAKE CROSSOVER

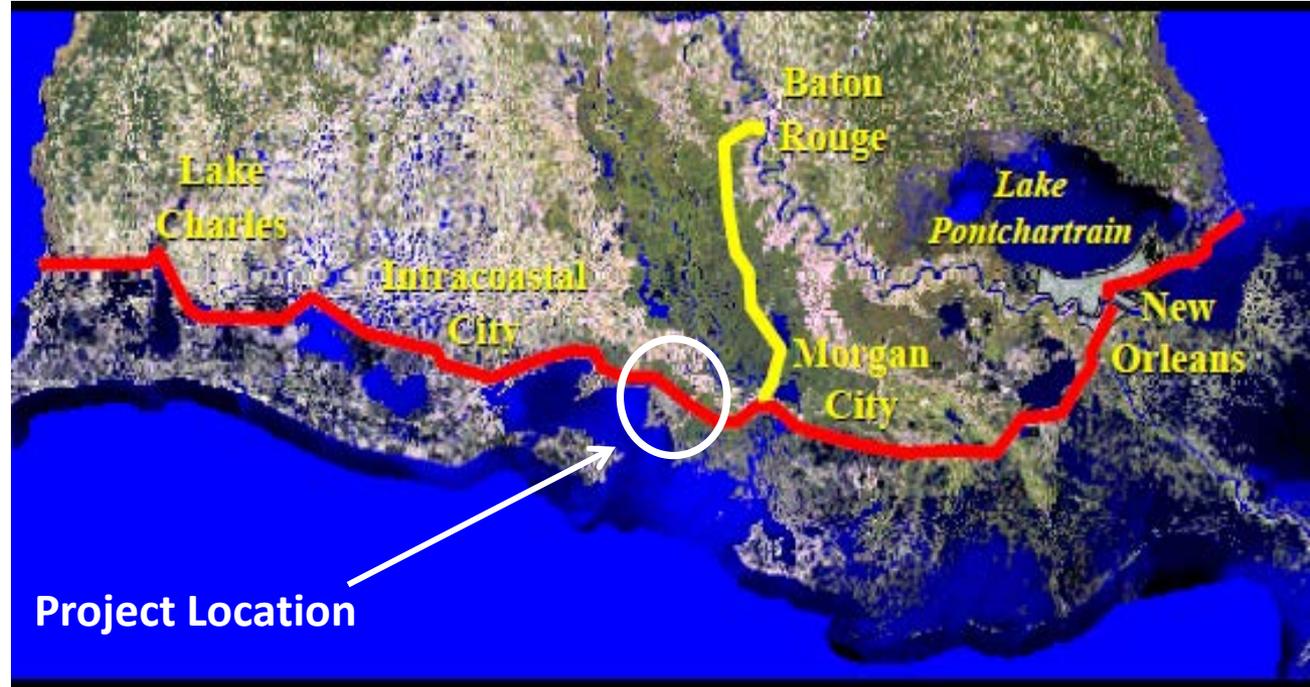

PROJECT AUTHORITY: The 384-mile-long GIWW was authorized by the Rivers and Harbors Acts of 1946 and 1962, and provides for a navigational channel across the State of Louisiana from the Rigolets in Lake Borgne to the Sabine River. A 12-foot-deep by 150-foot-wide channel is maintained in the first 33 miles from the Rigolets to New Orleans, Louisiana, and a 12-foot-deep by 125-foot-wide waterway is provided in the remainder of the mainstem.

Recent Dredging History Of Gulf Intracoastal Waterway – Wax Lake Crossover

Fiscal Year	Disposal Area	Dredging Quantity (CY)
2001	Wax Lake Outlet	63,319
	Open Water	86,164
2002	Wax Lake Outlet	141,562
	Open Water	122,607
2003	Wax Lake Outlet Open Water	131,604
2004	Wax Lake Outlet Open Water	173,005
2005	Wax Lake Outlet Open Water	88,964
2006	Wax Lake Outlet Open Water	17,393
2007	Wax Lake Outlet Open Water	141,100
2008	Wax Lake Outlet Open Water	119,800
2009	Wax Lake Outlet Open Water	251,479
2010	Wax Lake Outlet Open Water	133,115
2011	Wax Lake Outlet Open Water	228,896
2013	Wax Lake Outlet Open Water	91,820

