


**MISSISSIPPI RIVER, OUTLETS AT VENICE
BAPTISTE COLLETTE BAYOU
FY 2016 Maintenance Dredging**

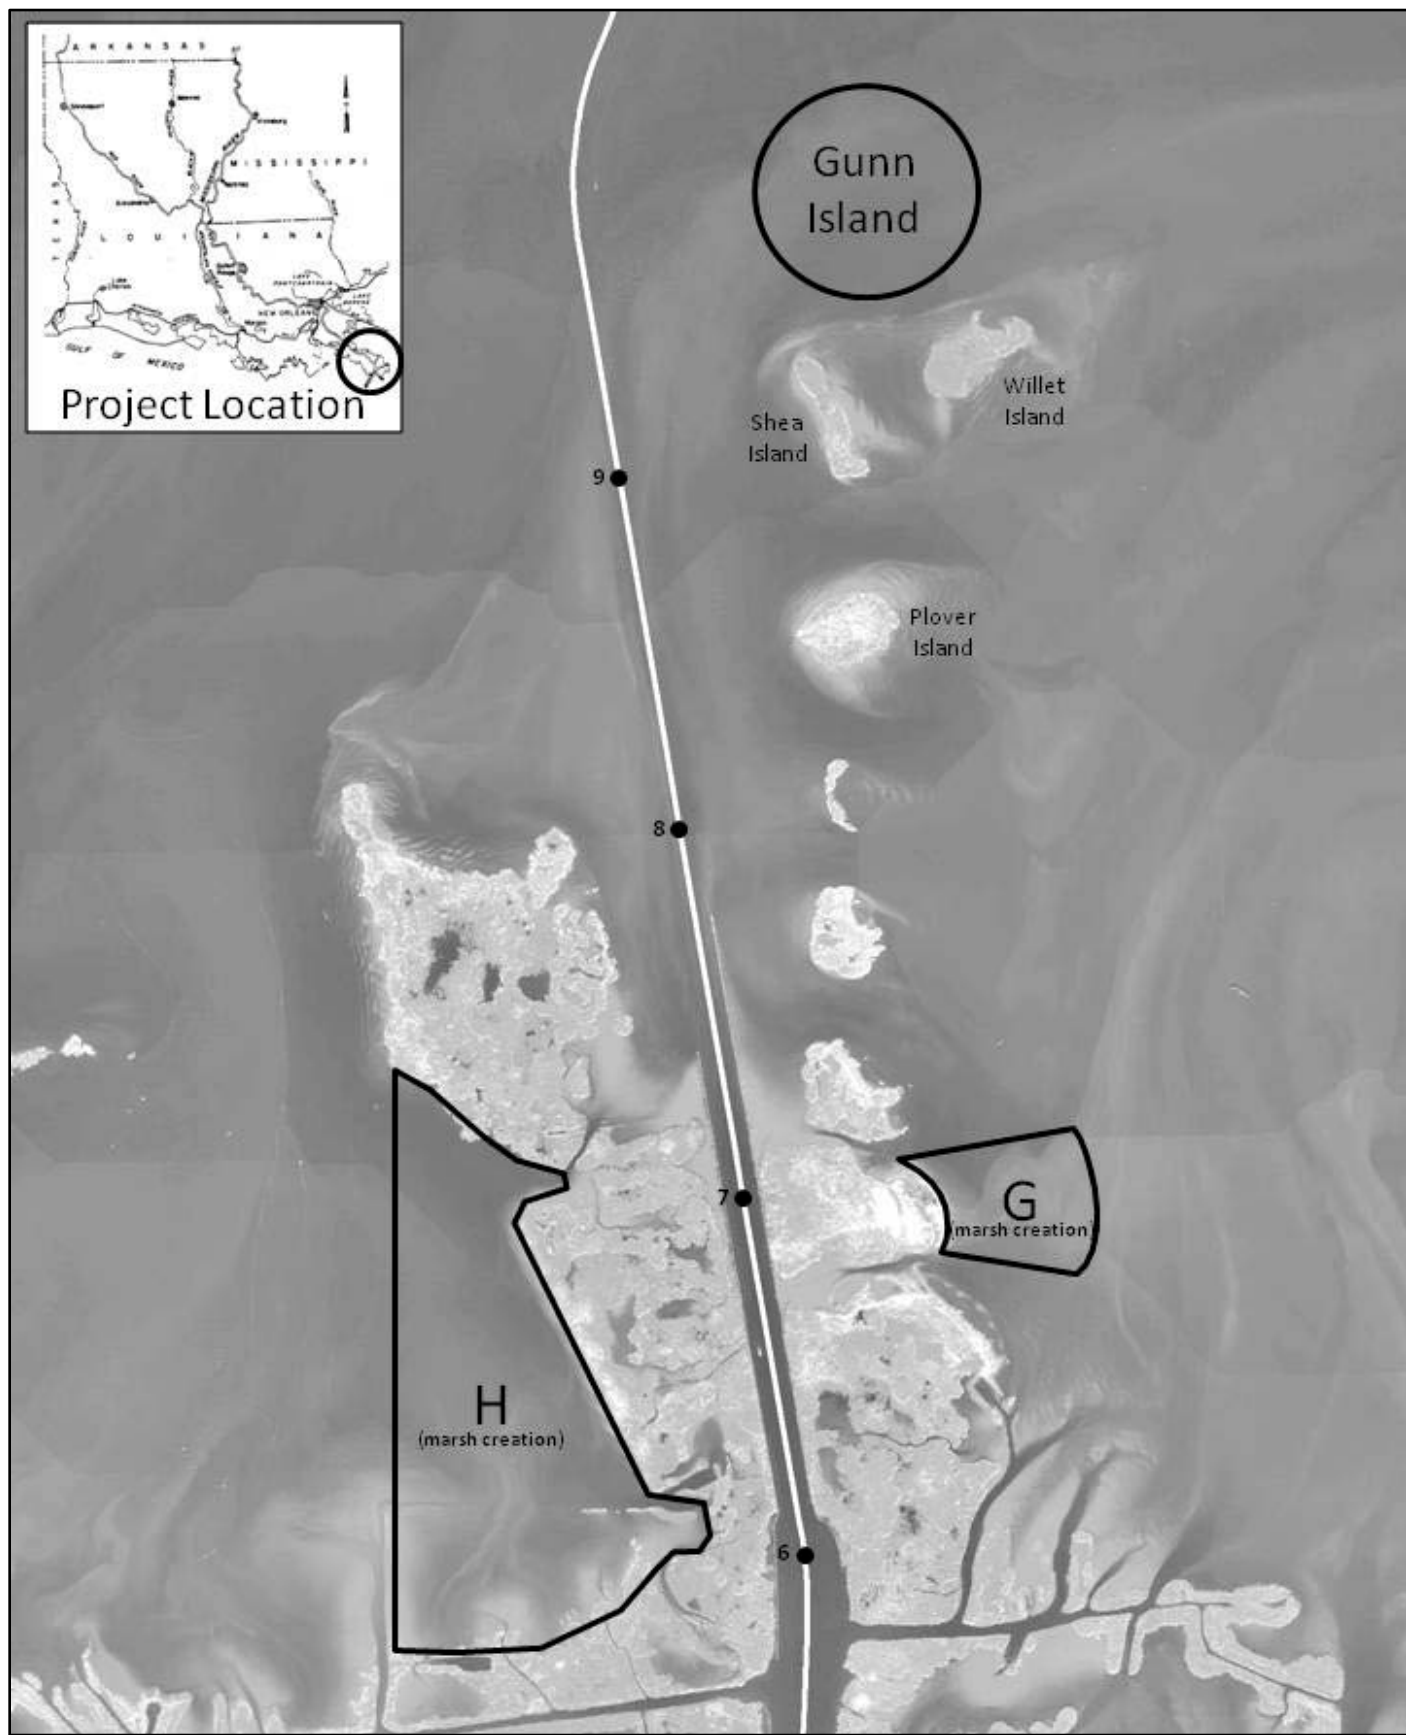

PROJECT	Mississippi River, Outlets at Venice, LA
DESCRIPTION OF WORK	Maintain a 16' deep x 250' wide channel in the jetty and bar channel (with an additional 2' of advance maintenance.)
OPERATIONS MANAGER	Ray Newman (504-862-2050)
LOCAL SPONSOR	Plaquemines Parish, LA

DREDGING FREQUENCY	Annual
LAST DREDGED	2014
TYPE OF DREDGE USED	Cutterhead

CONTRACT SCHEDULE	Advertise: Jul 2016	Open Bids: TBD	Award: TBD	Start Work: TBD	Duration: 90 days
ESTIMATED QUANTITY	400,000 to 1,600,000 CY				
ESTIMATED COST	\$4,000,000 - \$6,000,000				

DREDGING REACH	1) Mile 5.0 to 8.0 (Jetties) 2) Mile 8.0 to 10.5 (Bar Channel)
DISPOSAL AREAS	1) West/East side Breton Sound 2) East side Breton Sound
DISPOSAL TYPE	Open Water: Wetland Development and Create/Manage Bird Islands
SEDIMENT CHARACTERISTICS	Sand: 30% Silt-Clay: 70%

TYPE of BU PLACEMENT	REASON for NON-BU PLACEMENT
<input checked="" type="checkbox"/> Wetland Creation	Remote Location
<input checked="" type="checkbox"/> Bird Island	Unsuitable Material (Fluff)
<input type="checkbox"/> Beach Nourishment	Hopper Dredge Required
