FY14 Awarded, Ongoing, & Completed Dredging Work For New Orleans District (MVN)

http://www.mvn.usace.army.mil/od/navigation.asp

Last Updated 5/2/2014

Changes made since last update
Cutterheads
Hoppers
Dustpans

All scheduled information subject to change. Does not include contingency projects.

Dredging Performed
Contract Period = Bid Date + (Award/NTP Estimated Period) + Construction Duration Allowed

Project	Solicitation No.	Contract No.	Manager	Dredge	Dredge Start	Dredge End	Actual Bid Date	Notes
					Actuals			
OLD RIVER CONTROL STRUCTURE OUTFLOW CHANNELS	**13B0034**	**13C0026**	Beauvais	"Richard Laquay"	7/20/2013	1/9/2014	5/1/2013	13MVN200 Orion Marine. 1st NTP 29 May 2013, 2nd NTP 10 Jul 2013.
CALCASIEU RIVER MI 34 TO 15 MD	**13B0043**	**13C0031**	Falk	"Mike Hooks", "E. Stroud"	8/16/2013	3/21/2014	6/11/2013	13MVN180 Mike Hooks. Award 26 Jun 2013. NTP 9-Jul-2013. E.Stroud Commenced Ship Chann on 3-Dec-2013. E.Stroud Stopped 5-Feb-2014; Mike Hooks Stopped 7-Feb-2014. E.Stroud Resumed 16 Feb 2014.
MISS RIV HOH (HOUMA & BAPTISTE COLL) CDR 3-2013	**13B0019**	**13C0034**	Kornick, Landry, Schneider	"Borinquen", "Capt Frank"	7/21/2013	10/3/2013	7/10/2013	13MVN032 Bid Open 10-Jul-2013. Award 11 Jul 2013. NTP 16 Jul 2013. Capt Frank Replaced Borinquen on 16-Aug-2013.
ATCHAF BASIN, (GIWW) & MISC PROJECTS CDR IDIQ	**13B0055**	**13D0010**	Lowe, Landry, Beauvais	"Borinquen"	8/19/2013	10/12/2013	7/23/2013	13MVN065 Award 31 Jul 2013. NTP 2 Aug 2013, T.O. #1 Completed 25-Sep-2013, T.O. #2 Completed 12-Oct-2013.
MISS RIV SWP CUTTER CDR 1-2014	**14B0026**	**14C0023**	Kornick	"GD Morgan"	3/21/2014		2/4/2014	14MVN275 Weeks Marine Low Bidder. Award 10-Feb-2014. NTP 13 Feb 2014. Est End 15 Jul 2014.
MISS RIV NOH (HOUMA, LAFOURCHE, BAP COLLETTE) 2-14	**14B0021**	**14C0027**	Kornick, Schneider				4/15/2014	14MVN031 Mike Hooks low bidder. No New Orleans Harbor work. Award 16 Apr 2014. NTP 18 Apr 2014. Start 3 May 2014, EDC 29 Aug 2014.
MISS RIV SWP CUTTER CDR 2-2014	**14B0027**	**14C0028**	Kornick	"California"			4/15/2014	14MVN276 Great Lakes Low Bidder. Award 18 Apr 2014, NTP 23 Apr 2014. Estimated Start 14 May 2014, Estimated End 20 Jun 2014.

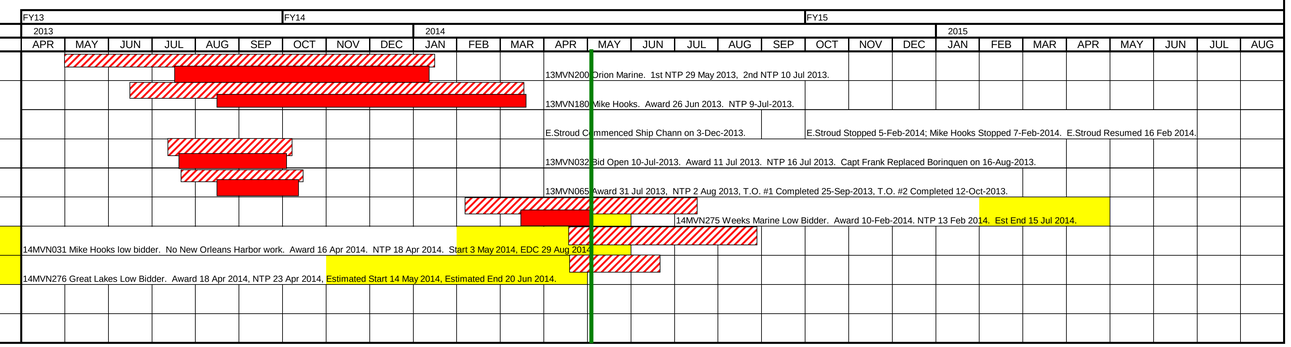

FY14 Awarded, Ongoing, & Completed Dredging Work For New Orleans District (MVN)

http://www.mvn.usace.army.mil/od/navigation.asp

Last Updated 5/2/2014

Changes made since last update
Cutterheads
Hoppers
Dustpans

All scheduled information subject to change. Does not include contingency projects.

Dredging Performed
Contract Period = Bid Date + (Award/NTP Estimated Period) + Construction Duration Allowed

Project	Solicitation No.	Contract No.	Manager	Dredge	Dredge Start (Actuals)	Dredge End (Actuals)	Actual Bid Date (Actuals)	Notes
MISSISSIPPI RIVER DEEP DRAFT CROSSINGS	W912EQ-12-R-0005/W912EQ-12-C-0011		Kornick	"Wallace McGeorge"	6/30/2013	12/13/2013		
MISSISSIPPI RIVER DEEP DRAFT CROSSINGS	**Gov't**		Kornick	"Jadwin"	6/29/2013	10/31/2013		
MISSISSIPPI RIVER SHALLOW DRAFT CROSSINGS	**Gov't**		Kornick	"Hurley"	9/1/2013	10/19/2013		
MISS RIV SWP GOV'T HOPPER	**Gov't**		Gov't	"McFarland"	8/7/2010	8/26/2010		
MISS RIV SWP GOV'T HOPPER EXERCISE	**Gov't**		Gov't	"Wheeler" A-SWP, B-Xings, C-NOH	4/29/2014			
MISS RIV SWP LSD HOPPER #3-2013	**13B0003**	**13C0028**	Kornick	"Newport", "Bayport"	6/10/2013	9/4/2013	5/30/2013	13MVN003 Manson Construction, Award 31-May-2013, NTP 4 Jun 2013. Bayport 17-Aug-2013 to 29-Aug-2013.
MISS RIV SWP LSD HOPPER #4-2013	**13B0004**	**13C0029**	Kornick	"Bayport"	6/7/2013	8/17/2013	6/4/2013	13MVN004 Manson Construction. Award 5Jun 2013.
MISS RIV SWP LSD HOPPER #5-2013 (CANCELLED)	**13B0005**	N/A	Kornick	N/A	N/A	N/A	6/19/2013	13MVN005 Over 25% of Government Estimate.
MISS RIV SWP LSD HOPPER #6-2013	**13B0006**	**13C0033**	Kornick	"Glenn Edwards"	7/18/2013	8/30/2013	6/25/2013	13MVN006 Manson, Award 28 Jun 2013, NTP 1 Jul 2013.
CALCASIEU RIVER BAR CHANNEL HOPPER #1-2013	**13B0035**	**14C0017**	Lowe	"Newport"	4/21/2014		1/7/2014	14MVN725 (OM-13-125) Manson-Low Bidder; Award 16 Jan 2014, NTP 3 Feb 2014, Estimated Complete 28 July 2014.
MISS RIV SWP LSD HOPPER #1-2014	**14B0003**	**14C0024**	Kornick	"Bayport"	3/9/2014		2/27/2014	14MVN001 Low Bidder Manson, Award 5 Mar 2014. EDC 26 May 2014.

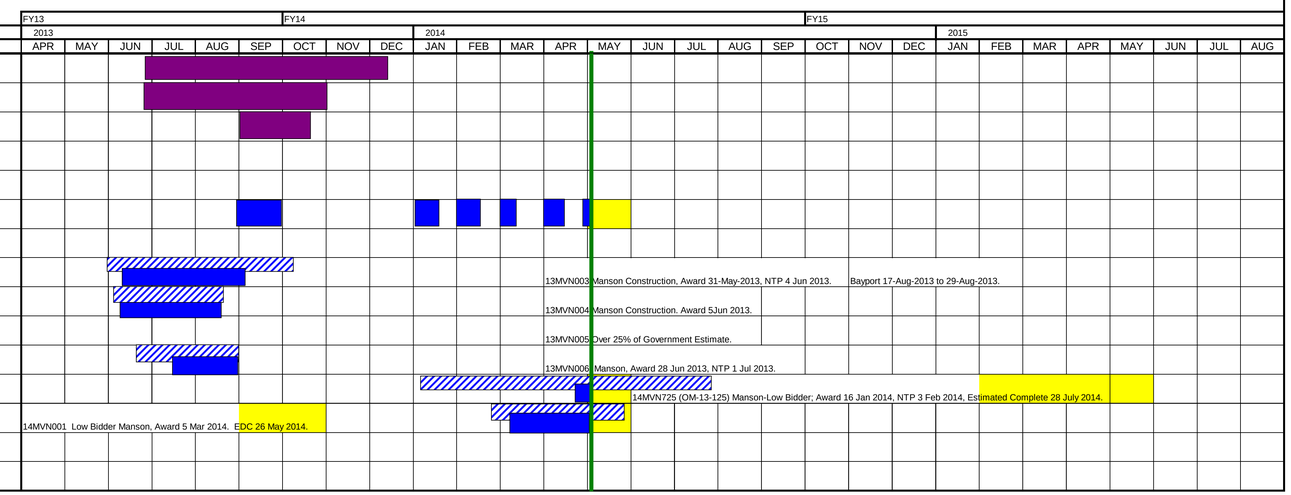

FY14 Awarded, Ongoing, & Completed Dredging Work For New Orleans District (MVN)

http://www.mvn.usace.army.mil/od/navigation.asp

Last Updated 5/2/2014

Changes made since last update
Cutterheads
Hoppers
Dustpans

All scheduled information subject to change. Does not include contingency projects.

Dredging Performed
Contract Period = Bid Date + (Award/NTP Estimated Period) + Construction Duration Allowed

Project	Solicitation No.	Contract No.	Manager	Dredge	Actuals: Dredge Start	Actuals: Dredge End	Actuals: Actual Bid Date
Lake Hermitage Marsh Creation (BA-42)	State of LA 2246811	LA Contract 3791647	USFWS/Kevin Roy 337-291-3120	"Marion"	2/24/2012		
Racoon Island Marsh Creation (TE-48B)	AG-7217-S-12-0009	AG-7217-C-12-0013	NRCS/Vicki Supler 318-473-7645	"E.W. Ellefson"	7/23/2012		
South Lake Lery Shoreline & Marsh Restoration (BS-16)			USFWS/Robert Dubois 337-291-3127		10/1/2013		4/1/2013
West Belle Pass Barrier Headland Restoration (TE-72)	State of LA 2244765	LA Contract 3748298	NMFS/Phillip Parker 225-578-8341	"Capt. Frank" "E.W.Ellefson"	2/18/2012	10/24/2012	
West Bay Sediment Diversion (MR-03)*	13B0016	13C0013	COE/Brad Inman 504-862-2124	"Missouri H"	3/4/2013	10/2/2013	2/5/2013

*CWPPRA project has an MVN maintenance dredging component
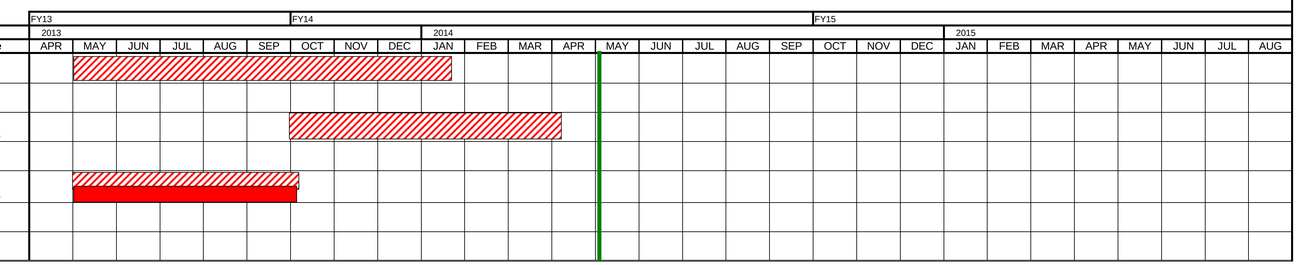
CWPPRA projects last updated 26 Feb 2013, S. Hennington
